(Umatilla River Anadromous Fish Habitat Project

Annual Report

January 1, 2019 – December 31, 2019

BPA Project Number 1987-100-01
Contract Numbers 73982 REL 60
January 2020

PREPARED BY:

Richard L. Christian & Mikayla Kelly

Confederated Tribes Umatilla Indian Reservation
Department Natural Resources Fish and Wildlife Programs
Nixyaawii Governance Center
46411 Timíne Way
Pendleton, Oregon 97801

Prepared for:
U.S. Department of Energy
Bonneville Power Administration
Division of Fish and Wildlife
P.O. Box 3621
Portland, Oregon 97208-3621

Suggested Citation:
Christian, R. L. & M. Kelly. 2020. The Umatilla Anadromous Fish Habitat Project: 2019 Annual Report. Confederated Tribes of the Umatilla Indian Reservation, report submitted to Bonneville Power Administration, Project No. 1987-100-01.

This report was funded by the Bonneville Power Administration (BPA), U.S. Department of Energy, as part of BPA's program to protect, mitigate, and enhance fish and wildlife affected by the development and operation of hydroelectric facilities on the Columbia River and its tributaries. The views in this report are the author's and do not necessarily represent the views of BPA.

ACRONYMS

BA	biological assessment
B&G	Bauer & Gustafson
BDSS	beaver dam support structure
BIA	Bureau of Indian Affairs
BPA	Bonneville Power Administration
cfs	cubic feet per second
COTR	Contracting Officer Technical Representative
CREP	Conservation Reserve Enhancement Program
CTUIR	Confederated Tribes of the Umatilla Indian Reservation
cy	Cubic Yards
dbh	diameter at breast height
EPA	United States Environmental Protection Agency
ESA	Federal Endangered Species Act
ft	foot/feet
FY	fiscal year
in	inch/inches
JPA	Joint Permit Application
km	kilometer/kilometers
LWD	large woody debris
m	meters
mi	mile/miles
MOA	Memorandum of Agreement
NOAA	National Oceanic and Atmospheric Administration
NMFS	National Marine Fisheries Service
NPPC	Northwest Power Planning Council
NPCC	Northwest Power and Conservation Council
NRCS	Natural Resource Conservation Service
ODA	Oregon Department of Agriculture
ODEQ	Oregon Department of Environmental Quality
ODFW	Oregon Department of Fish and Wildlife
ODSL	Oregon Department of State Lands
OWEB	Oregon Watershed Enhancement Board
OWRD	Oregon Water Resources Department
PCSRF	Pacific Coastal Salmon Recovery Fund
RM	river mile
SOW	Statement of Work
SE	Standard error
TMDL	total maximum daily load
UBAFHP	Umatilla Basin Anadromous Fisheries Habitat Project
UBNPME	Umatilla Basin Natural Production Monitoring and Evaluation Project
UBWC	Umatilla Basin Watershed Council
USDA-FS	United States Department of Agriculture Forest Service
USFWS	United States Fish and Wildlife Service
USGS	United States Geological Survey
UPRR	Union Pacific Railroad

TABLE OF CONTENTS

LIST OF FIGURES ..... **I**

LIST OF TABLES ..... **II**

INTRODUCTION **1**

PROJECT AREA 5

COMPLETED WORK **8**

CONTRACT 73982 REL 60 (CY 2019) 8
DISCUSSION 24

LESSONS LEARNED AND ADAPTIVE MANAGEMENT **26**

LESSONS LEARNED 26
ADAPTIVE MANAGEMENT 27

SUMMARY AND CONCLUSIONS **29**

LITERATURE CITED **36**

APPENDIX A: USE OF DATA AND PRODUCTS **45**

APPENDIX B: LIST OF METRICS AND INDICATORS **46**

LIST OF FIGURES

FIGURE 1. UMATILLA RIVER SUBBASIN 6
FIGURE 2. UMATILLA RIVER BASIN FY 2019 UBAFHP PROJECT SITES. 7
FIGURE 3. CTUIR SEMI-ANNUAL REPORT FOR THE UMATILLA SUBBASIN FISH HABITAT RESTORATION PROJECT, AUGUST – DECEMBER, 2019. 11
FIGURE 4. UBAFHP OUTREACH AND EDUCATION ACTIVITIES. CTUIR COMMUNITY MEMBERS LEARNING ABOUT DNR PROJECTS AT THE ANNUAL OPEN HOUSE (LEFT); UPRR TOUR OF MEACHAM CREEK DURING HIGH FLOWS IN APRIL (RIGHT). 12
FIGURE 5: ATHENA BRIDGE FISH PASSAGE PROJECT BEFORE AND AFTER CONSTRUCTION 16
FIGURE 6: UMATILLA RIVER AT THE REITH DAM SITE, BEFORE, DURING, AND AFTER CONSTRUCTION. 18
FIGURE 7. BEFORE (2018) AND AFTER (2019) PHOTOS OF THE MEACHAM CREEK FLOODPLAIN RESTORATION AND IN-STREAM ENHANCEMENT PROJECT AREA 2 TAKEN AT PHOTO POINT MONITORING LOCATIONS. 19
FIGURE 8: CTUIR PLANTING NATIVE VEGETATION AT THE MEACHAM CREEK PROJECT SITE (LEFT) AND THE ATHENA BRIDGE PASSAGE PROJECT AT WILDHORSE CREEK (RIGHT) 20
FIGURE 9: ORIGINAL PLAN FOR BEAVER DAM ANALOG INSTALLATION (LEFT). INSTALLATION OF TREE BRUSH MATS (RIGHT). 22

LIST OF TABLES

TABLE 1. SUMMARY OF IMPLEMENTATION WORK ACCOMPLISHED IN 2019.....3
TABLE 2. MAJOR DESIGNS AND PROJECT PLANNING FOR THE 2019 FIELD SEASON.....4
TABLE 3. HABITAT PASSAGE STRUCTURES MONITORED AND MAINTAINED BY CTUIR TO MEET DESIGN SPECIFICATIONS.....13
TABLE 4. NOXIOUS WEED TREATMENTS COMPLETED BY LOCATION WITHIN THE UMATILLA RIVER BASIN, 2019.....14
TABLE 5. MEACHAM CREEK BONIFER REACH IMPLEMENTATION SCHEDULE.....19
TABLE 6. INVASIVE WEED SPECIES DETECTED IN MEACHAM CREEK FLOODPLAIN RESTORATION AND IN-STREAM ENHANCEMENT PHASE I AND II PLANTING AREAS IN 2016 AND RELATIVE PRIORITY FOR CONTROL EFFORTS.....22
TABLE 7. THE UMATILLA ANADROMOUS FISH HABITAT PROJECT OBJECTIVES RELATIVE TO THE UMATILLA RIVER VISION TOUCHSTONES (JONES ET AL. 2008), BPA 2008 FISH ACCORDS PRIMARY LIMITING FACTORS (FISH ACCORDS 2008) AND NOAA'S ECOLOGICAL CONCERNS (NMFS 2009).....24
TABLE 8. THE CTUIR UBAFHP RESTORATION PROJECT DESCRIPTIONS BY LOCATION, TREATED PRIMARY LIMITING FACTORS (NMFS 2009) BY CTUIR RIVER VISION TOUCHSTONES (JONES ET AL. 2008) AND ACCOMPLISHMENTS; 2007-2019.....31

INTRODUCTION

The CTUIR retain aboriginal and treaty rights related to fishing, hunting, pasturing of livestock, and gathering of traditional plants within the Umatilla River Subbasin. The CTUIR Department of Natural Resources (DNR) has developed and accepted a First Foods organization and approach to ecosystem management based on the cultural traditions and practices of the Longhouse. The organization follows the serving order of food and conceptually "Extends the Table" to manage for sustainability within the Umatilla River Subbasin. The First Foods are considered to be the minimum ecological products necessary to sustain CTUIR culture (Quaempts et al. 2018). The order is watershed-based beginning with water at the first and lowest point and progresses up to salmon, deer, cous, and huckleberry. This creates clear links to treaty rights and resources and sets direction and goals that relate to the community culture. In addition the DNR developed the Umatilla River Vision that provides a description of the processes and conditions needed to protect and provide for First Foods. The River Vision describes physical and biological processes in support of 5 touchstones; hydrology, geomorphology, connectivity, riparian vegetation, and aquatic biota. The work accomplished through this project is directly related to the First Foods of water and salmon and the 5 touchstones, which incorporates goals of restoring high water quality and healthy and sustainable salmonid fish populations.

CTUIR's right to fish in its historical fishing places was acknowledged in the Treaty of 1855 that stated: "the exclusive right of taking fish in the streams running through and bordering said reservation is hereby secured to said Indians, and at all other usual and accustomed stations…" (Treaty of 1855, Articles of Agreement, Article 1, page 3). Decreased salmonid abundance has significantly impacted the livelihood of the Tribal community and altered their way of life.

Overfishing, sweeping changes to rivers and streams, and policies that changed the landscape have endangered salmon and created a "salmon crisis" (Montgomery 2003). It is the challenging duty of the CTUIR Umatilla Basin Anadromous Fisheries Habitat Project (UBAFHP) to restore and sustain healthy conditions of local watersheds to both assist in salmon recovery and ensure they provide adequate quantities of sustainable natural resources to satisfy the CTUIR's needs and preserve opportunities for traditional ways of life.

As part of the Northwest Power Conservation Council's Columbia Basin Fish and Wildlife Program, this project is one of Bonneville Power Administration's (BPA) many efforts at off-site mitigation for damage to salmon and steelhead runs, their migration, and wildlife habitat caused by the construction and operation of FCRPS dams. The Umatilla Anadromous Fish Habitat Project (UBAFHP; #1987-100-01) initiated by CTUIR in 1987 is an integral component of the Umatilla River Subbasin Salmon and Steelhead Production Plan (NPPC 1990), and project work is supported both locally and regionally by multiple planning documents: Umatilla/Willow Subbasin Plan (NPCC 2005), Umatilla River Basin TMDL and Water Quality Management Plan (2001), CTUIR TMDL (2005), Umatilla River Vision (Jones et al. 2008; Existing Project Document ID: P130339), Conservation and Recovery Plan for Oregon Steelhead Populations in the Middle Columbia River Steelhead Distinct Population Segment (NMFS 2009), Recovery Plan for the Coterminous United States Population of Bull Trout (*Salvelinus confluentus*) (USFWS 2015), Meacham Creek Watershed Analysis and Action Plan (Andrus and Middel 2003), Umatilla and Meacham Watershed Assessment (UNF 2001), and the Birch Creek Watershed Action Plan (CTUIR 2016).

The Final Umatilla/Willow Subbasin Plan (NPCC 2005; Subbasin Plan) provided a systematic vision of a healthy ecosystem with abundant, productive, viable, and diverse populations of aquatic and terrestrial species with goals, objectives, and management strategies necessary to reach the subbasin vision. The vision entails several broad goals for habitat: 1) Protect existing high quality fish and wildlife habitat and strongholds, 2) restore and enhance degraded and diminished fish and wildlife habitats to support population restoration goals and to mitigate impacts from the construction and operation of the Columbia basin hydropower system and other anthropogenic impacts, and 3) restore the health and function of ecosystems in the Umatilla subbasin to ensure continued viability of their natural resources (Management Plan, page 5-3). Specific aquatic qualitative objectives and strategies were developed in to support the

subbasin vision and goals. Quantitative management objectives relative to the UBAFHP work activities include 1) maintain and enhance natural production, productivity, abundance, life history characteristics and genetic diversity of fish and mussels throughout the Umatilla Subbasin using habitat protection and improvement and 2) maintain and enhance passage of adult and juvenile steelhead and Chinook throughout the Umatilla Subbasin with passage protection and restoration (Management Plan, page 5-5). The Umatilla Subbasin Plan (NPCC 2005) determined that the limiting factors could be addressed through habitat restoration and implementation ("Phase III") of the Umatilla Basin Project (pages 5-10). An identification and analysis of limiting factors/conditions and priority areas for action are fully described within the Subbasin Plan (Section 3.5) including passage barriers/entrainment, in-channel characteristics, habitat diversity (LWD), floodplain confinement, high water temperatures, high turbidity, inadequate flows, and poor riparian/floodplain vegetation. Priority management strategies are being conducted by the UBAFHP in accordance with the Final Umatilla Willow Subbasin Plan (NPCC 2005; pages 5-8 & 5-9) to address limiting factors within the subbasin:

- Increase water conservation and irrigation efficiency
- Large Wood/Boulder Structure Placement
- Fence/Plant Riparian Zones
- Modify Channel Floodplain Function
- Construct Pool/Riffle – In-stream Modification
- Modify Detrimental Land use Activities
- Restore Upstream/Headwater Attributes to Improve Downstream Conditions
- Increase Passage Efficiency

The UBAFHP continues to protect, enhance, and restore functional floodplain, channel, and watershed processes to provide sustainable and healthy habitat for aquatic species in the Umatilla River Subbasin. Habitat restoration efforts fit within a holistic watershed approach supporting capacity building and long-term progress towards 1) achievement of the CTUIR DNR River Vision and First Foods mission statements, 2) Endangered Species Act delisting of Columbia River bull trout and middle Columbia River steelhead, and 3) addresses water quality limiting factors per the Clean Water Act 303d list.

During the 31-year project history, the CTUIR has helped administer and implement a number of fisheries habitat enhancement projects in the Umatilla River Subbasin. The CTUIR maintains partnership habitat enhancement projects along Meacham Creek, Isquúlktpe Creek, Birch Creek, Wildhorse Creek, East and West Birch Creek and the mainstem Umatilla River, among other sites. The CTUIR has developed effective interagency partnerships and is effectively working at the policy and project levels with various federal, state, and county agencies and private landowners.

The UBAFHP is an integral component of the *Umatilla River Subbasin Salmon and Steelhead Production Plan* (1990) and is well integrated into the framework of the *Umatilla Subbasin Plan* (NPCC 2005) established by the NPCC to better coordinate habitat restoration work in the Umatilla River Basin. The CTUIR, ODFW, Natural Resource Conservation Service (NRCS), Umatilla National Forest, Umatilla Basin Watershed Council (UBWC), and other participating agencies and organizations have made significant progress towards restoring and protecting vital salmonid habitat in the basin.

The major project accomplishments during the 2019 contract periods are described in Table 1 below. This only includes the major implementation activities. The planning and design related activities for future implementation projects are contained in Table 2.

Table 1. Summary of Implementation work accomplished in 2019.

Work Element	Location	Description
Conservation Agreements	Wildhorse, Birch, EFK Birch, WFK Birch, Cottonwood, & Umatilla River	Maintain current conservation agreement terms and conditions on 17 agreements, including maintaining fencing and watering plantings.
Weed Treatment	Meacham Creek	Controlled noxious weeds on 55 acres of conservation agreements and previously implemented habitat projects using chemical and mechanical treatments. Biological control treatments are ongoing.
Planting	Meacham Creek	6956 plants installed.
	Wildhorse Creek	375 plants installed.
Meacham Creek – Bonifer Project (Project Area 2)	Meacham Creek	Constructed 7,656 linear feet of stream channel and installed 300 pieces of large wood (plus tops) individually and in 24 engineered log jams.
Reith Dam Removal	Umatilla River	Collaborated with private landowners and the UBWC to remove the Wyss Dam on the mainstem Umatilla River.
Athena Fish Passage Mitigation	Wildhorse Creek	Installed a prefabricated modular bridge at the crossing of 3rd Street and Wildhorse Creek in Athena, OR to rectify a major passage barrier.

Table 2. Major designs and project planning for the 2019 field season.

Project	Description
Athena Fish Passage Mitigation	Completed an engineered design to remove a fish passage barrier and construct a roughened riffle passage channel through the project reach on Wildhorse Creek. Partnered with the UBWC and ODFW to produce designs for a prefabricated, modular concrete bridge structure to replace the current passage barrier.
East Birch Creek Floodplain Restoration and In-stream Enhancement Project	Continue the design process to produce an engineered design for a floodplain reconnection and in-stream habitat enhancement project on East Birch Creek. Design anticipated to be completed in 2020 and implementation in 2020.
Reith Dam Removal Design	Collaborated with BPA engineering staff to produce an engineered design for removal of the defunct Reith Dam on the mainstem Umatilla River. Design completed early 2019 and implementation took place during the 2019 in-water work window.
UmaBirch Conservation Easement	Collaborated with the landowner and continued tasks to complete a conservation easement on the UmaBirch property. Conservation Easement anticipated to be completed in 2020.
UmaBirch Design	Selected design firm and completed 60% designs for a piece of the UmaBirch Project. The design for Birch Creek 2.3 will be taken to 100% and construction will begin in 2020. The remainder of the project will be fully designed in 2020 with implementation anticipated, beginning in 2021.
UmaBirch NEPA Compliance	An environmental assessment was initiated in 2019 and is anticipated to be completed by mid-summer 2020.
Umatilla River Assessment	Began collecting existing data, identifying data gaps, and scoping the assessment within CTUIR. Assessment anticipated to be initiated in 2020.

Project results are reported in various BPA formats including Pisces status reports, project completion reports, and annual reports. The CTUIR maintains a complete database on project planning, proposals, permitting, implementation, and results through the completion of required project deliverables. For a complete list of reports submitted by the CTUIR's UBAFHP since 1989, please consult the following website at URL: http://www.efw.bpa.gov/integratedfwp/reportcenter.aspx.

Project Area

The UBAFHP is defined by the boundaries of the Umatilla River Subbasin, which is located in the northwest portion of the Blue Mountain Ecological Province in northeast Oregon. The Umatilla River Subbasin comprises 1,465,600 acres of the 6,400,000 acres of ceded CTUIR land (CTUIR 1995) as identified by the Treaty of 1855. Figure 1 illustrates the vicinity of the Umatilla River Subbasin within the Blue Mountain Province (Project map: *http://www.cbfish.org/Project.mvc/Map/1987-100-01).* The Umatilla River drains an area of approximately 2,540 square miles (mi.^{2}) (6,579 square kilometers [km^2]) and flows approximately 89 mi. (143 km) from where it branches into the north and south forks of the Umatilla River to the mouth at the confluence with the Columbia River. Each fork adds another approximately 10 mi. (16 km) of length. The Umatilla River originates at elevations up to 4,228 feet (ft.; 1,289 m) and flows west and north to its confluence with the Columbia River (USFWS 2002) at an elevation of about 269 ft. (82 m).Other major tributaries include Meacham Creek, Birch Creek, McKay Creek, Butter Creek, and Wildhorse Creek.

The Umatilla River Subbasin historically supported viable and harvestable populations of spring/summer and fall Chinook salmon (*Oncorhynchus tshawytscha*), coho salmon (*O. kisutch*), sockeye salmon (*O. nerka*), summer steelhead (*O. mykiss*), Pacific lamprey (*Entosphenus tridentatus*), bull trout (*Salvelinus confluentus*), steelhead-rainbow trout (*O. mykiss sp*.), mountain whitefish (*Prosopium williamsoni*) and a variety of additional native species. Anthropomorphic alterations have negatively impacted the watershed and caused significant reductions of endemic salmonid populations. Beginning in the late 1800s, fish populations started to decline due to habitat degradation. In fact sockeye and coho were extirpated by the early 1900s. Irrigation and agricultural development throughout the basin in the early 1900s is believed to be the primary cause of the decline of steelhead and the extinction of salmon. Since the signing of the Treaty of 1855, aquatic and riparian habitats have been degraded through irrigation diversions, water extractions, channelization, livestock grazing, logging, agriculture and urban development (NPCC 2004). Subsequently, the abundance of Chinook, steelhead, bull trout, and other fish species has also been dramatically reduced. The Umatilla River population of spring Chinook salmon was reported extinct in 1926 (Boyce 1986). With declining fish populations, Tribal governments, federal, state and international agencies were obligated to eliminate or significantly reduce subsistence and sport fisheries by the mid-1970s. The Federal government listed Middle Columbia River summer steelhead and Columbia River bull trout in the Umatilla Subbasin as threatened species under the ESA in 2006 and 1999, respectively.

In the mid-1980s, a successful, hatchery-based salmonid reintroduction effort for the Umatilla River was instituted using neighboring strains of various salmonid species. Although hatchery programs currently support subsistence and restricted sport fishing opportunities for steelhead and Chinook and coho salmon, there remains significant need to re-build viable, harvestable, and sustainable naturally-produced fish stocks throughout the basin.

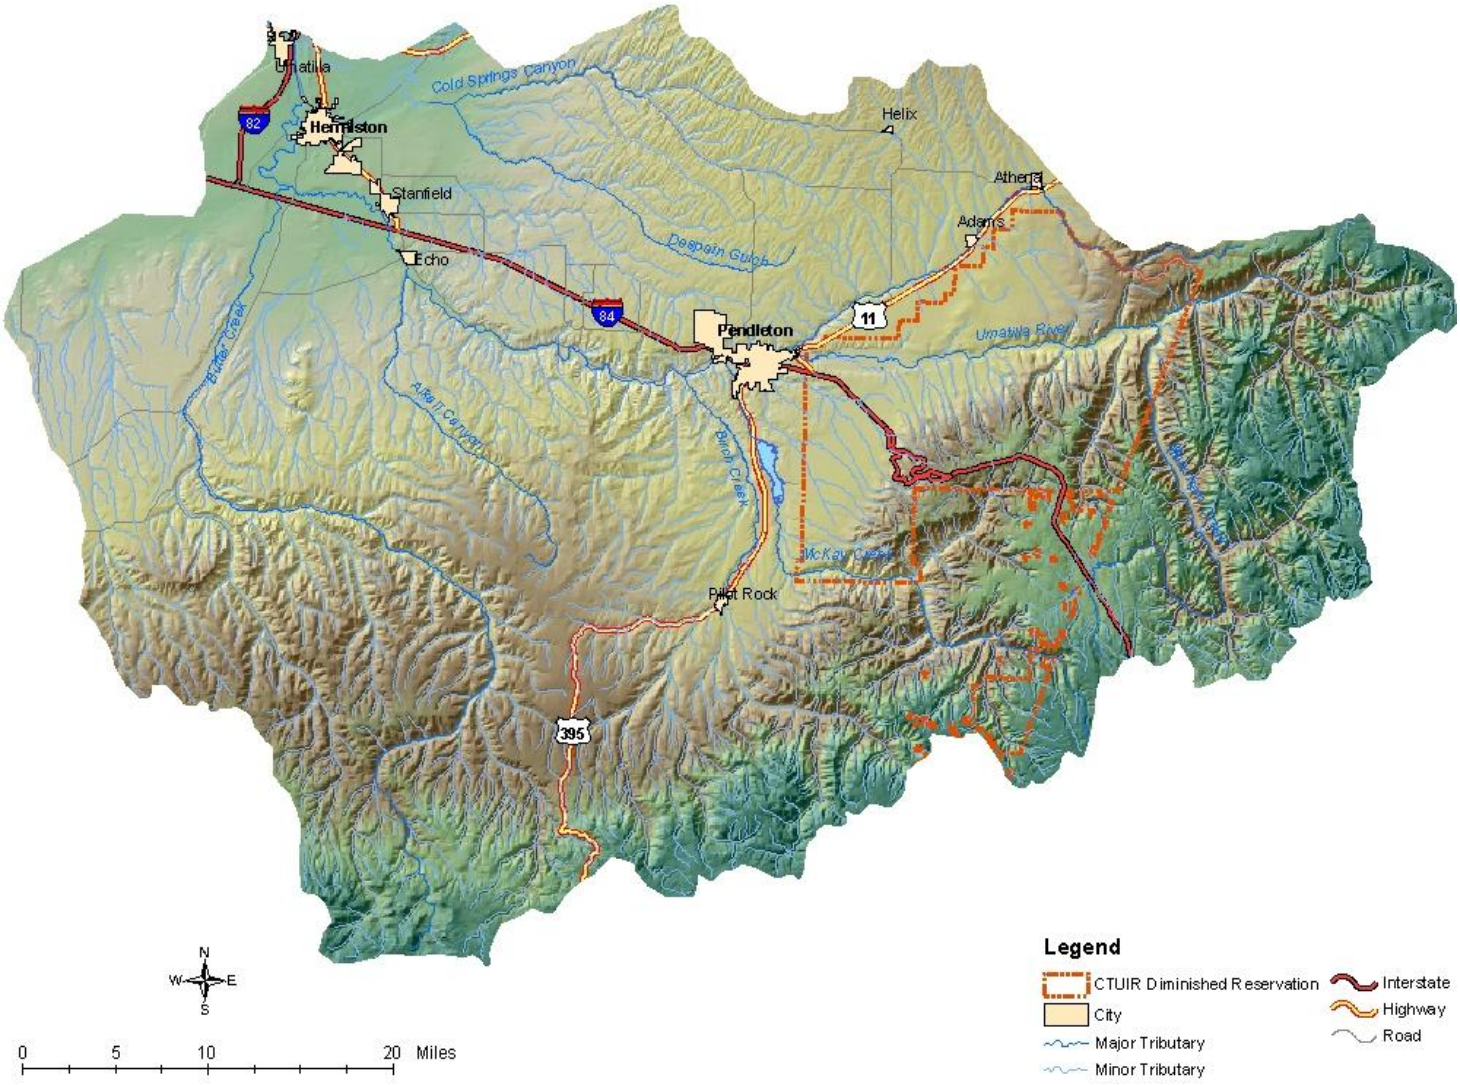


Figure 1. Umatilla River Subbasin

Our primary area of focus for restoration and monitoring work in FY 2019 was Meacham Creek, Wildhorse Creek, Birch Creek and mainstem Umatilla River (Figure 2).

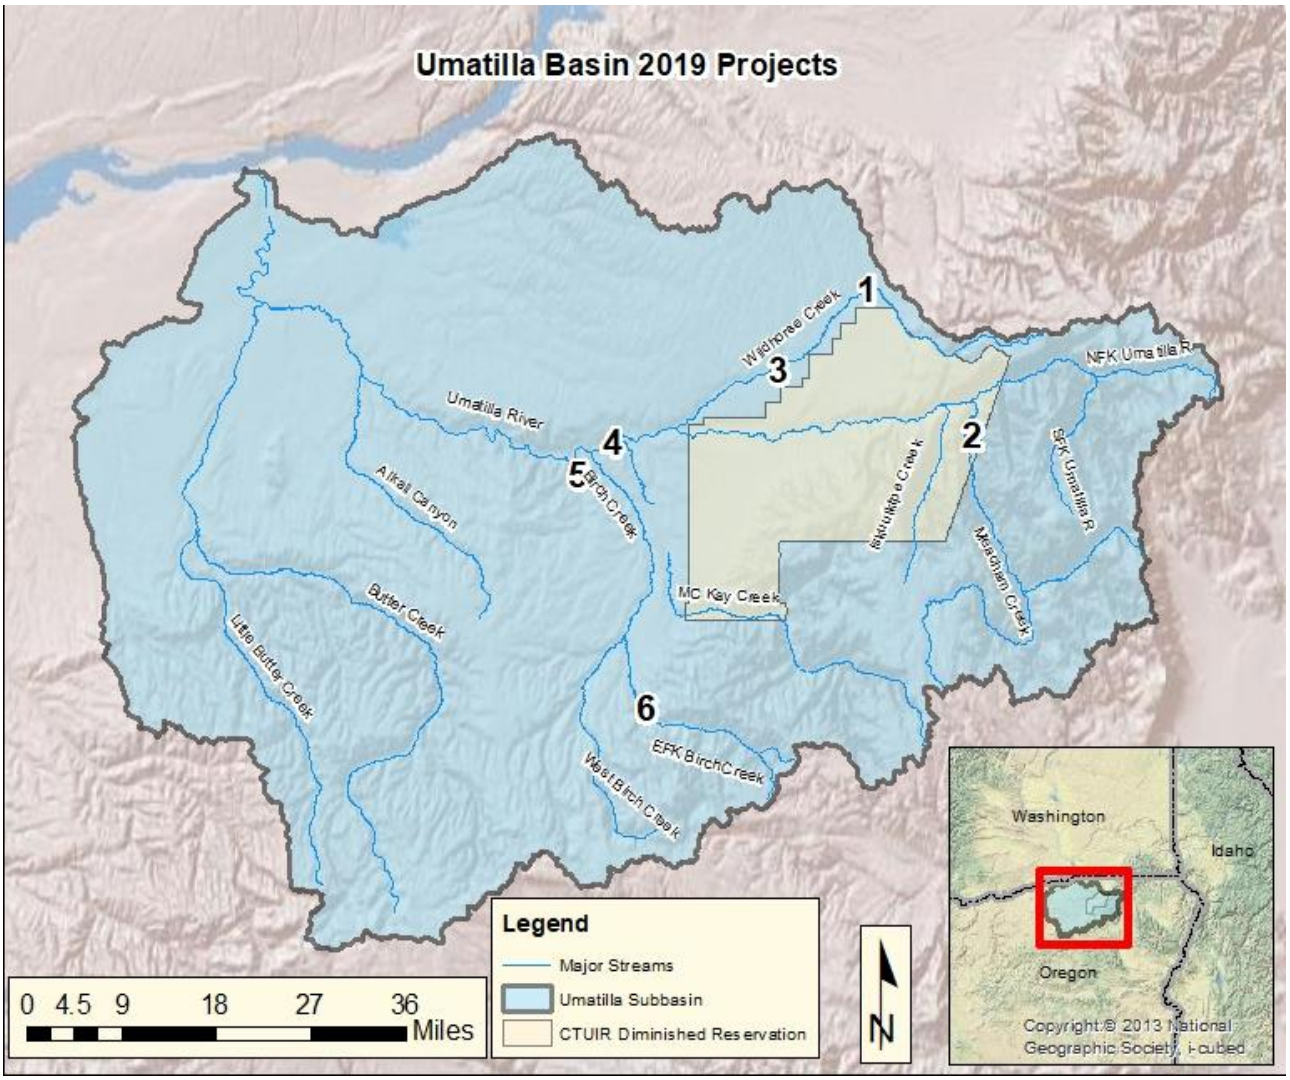


Figure 2. Umatilla River Basin FY 2019 UBAFHP Project Sites

1: Wildhorse Creek Fish Passage Rectification (Athena Bridge): Fish passage rectification and bridge replacement at 3rd Street crossing.

2: Meacham Creek (Bonifer Reach): Constructed nearly 1 mile of full floodplain restoration on Meacham Creek (Project Areas 2).

3: Wildhorse Creek: Additional weed treatment and beaver dam analog site.

4: Reith Dam Removal: Collaborated with partners to complete irrigation diversion change and complete full dam removal on the mainstem Umatilla River.

5: UmaBirch CE/Design: Worked toward a conservation easement to protect over 360 acres of floodplain at the confluence of the Umatilla River and Birch Creek. Concurrently developing a restoration design.

6: East Birch Creek Floodplain Restoration Design: Worked collaboratively with private landowner to execute a conservation agreement and design a floodplain restoration project on their property.

COMPLETED WORK

This section highlights and describes completed work elements in an outline similar to our statement of work on CBFish.org. Each work element with associated identifier code and milestone are listed, followed by a comprehensive summary of completed work under each work element. In addition to a description of completed work elements specific to restoration activities, we briefly highlight habitat inventory results specific to UBAFHP efforts outlined for this contract period.

Contract 73982 REL 60 (CY 2019)

Work Element A: 119. Manage and Administer Projects
Work Element Title: Manage and Administer Project
Milestone Deliverable: Effective implementation management and timely contract administration

A. Evaluate current workload and monitor implementation progress.
B. Develop work plan consistent with expected budget availability and potential tasks or projects.
C. Integrate and manage the planning, permitting, environmental compliance, and coordinated implementation of contract actions.

This work element includes general administration of the CTUIR Umatilla Anadromous Fish Habitat Project (UAFHP). CTUIR staff managed and administered project activities in accomplishing work elements and milestones with associated costs.

Work Element B: 185. Produce Pisces Status Report
Work Element Title: Periodic Status Reports for BPA
Milestone Deliverable: Complete Periodic Pisces Status Reports

CTUIR reported to BPA periodically during the contract period on the status of each statement of work element, and milestones and deliverables using the computer program Pisces:
February-June (2/1/2019 - 6/30/2019)
July-September (7/1/2019 - 9/30/2019)
October-December (10/1/2019 - 12/31/2019)
Final January (1/1/2020 - 1/31/2020)

The BPA Contracting Officer Technical Representative (COTR) reviewed the Pisces status reports, recommended changes as necessary and accepted them electronically upon approval. Additionally, upon completion of each deliverable milestone, we provided metrics and final project location (latitude and longitude) when required. These Pisces status reports provide a tool for the BPA COTR and administrative staff to track project progress in meeting contract requirements.

Work Element C: 165. Produce Environmental Compliance Documentation
Work Element Title: Produce Environmental Compliance Documentation
Milestone Deliverable: Receipt of Environmental Compliance Clearance from BPA

The following milestones were completed for FY 2019 projects:

- Meacham Creek – Bonifer Reach Floodplain Reconnection
- Mainstem Umatilla River – Reith Dam Removal

- Wildhorse Creek – Athena Bridge Fish Passage Improvement

CTUIR successfully submitted many applicable documents to the appropriate federal, tribal, state, county entities for select implementation projects in a timely manner required under work elements related to producing environmental compliance documentation in FY2019. Secondary environmental compliance accomplishments during the reporting period included coordination with various compliance personnel to prepare supplemental documentation and reporting for ongoing and planned management actions. Environmental compliance methods include development of appropriate documentation under various federal, Tribal, state and county laws and regulations governing federally funded project work. Methods involve coordination with various federal and state entities agencies and development and submittal of permit applications, cultural clearances, biological assessments, National Environmental Policy Act checklists, etc., as necessary. Part of the environmental compliance work element includes planning and developing site-specific proposals tailored to accomplish fisheries goals and meet compliance standards. The details concerning the implementation of treatments and preparations for putting efforts on the ground, including preparations for subcontracting, and specifics in regarding the safeguarding of ESA-Listed species during the implementation process are outlined in the proposals.

1) UBAFHP Environmental Compliance Documentation
2) ESA consultation with NMFS for FY 2019 project activities was covered under the Terms and Conditions of the HIP III Programmatic Biological Opinion (HIP III BO). Project activities covered under the HIP III BO included:
3) Operate and Maintain Habitat/Passage/Structure (WE I: 186; WE J: 186): CTUIR monitored and maintained existing easements and habitat improvement sites. Maintenance included vegetation watering and installing bioengineering treatments to stabilize habitat features.
4) Maintain/Remove Vegetation (WE K: 198): Project activities included watering and maintaining plants on NRCS CREP tracts and treating noxious weeds.
5) Plant Vegetation (WE T: 47): Project activities included planting in the newly constructed Meacham Creek Bonifer Reach project (RM 3.2-3.8) and in the previously constructed Meacham Creek Phase 3-4 project are (RM 3.8-5.7).
6) Install Fish Passage Structure (WE L: 184): CTUIR assisted in completing environmental compliance for the removal of Reith Dam on the mainstem Umatilla River (RM 48.2).
7) Meacham Creek Construction (WE R: 29; WE S: 30): CTUIR continued implementation of a nearly 4-mile reach of full floodplain restoration on Meacham Creek. Project activities included side channel construction, off-channel habitat construction, and large wood addition.

CTUIR submitted a letter and attachments with necessary project descriptions and geo-referenced maps for assisting BPA with Section 106 National Historic Protection Act consultations and environmental compliance. The following projects were submitted for compliance:

1) Reith Dam Removal Fish Passage Improvement Project – Dam Removal
2) UmaBirch Floodplain Restoration and In-stream Enhancement
3) East Birch Creek RM 5.3-5.8 Habitat Enhancement Project

Cultural Resources protection and preservation compliance was ongoing during this contract period. The CTUIR Cultural Resources Protection Program is anticipated to deliver a final report to BPA in early 2020. As well as the projects listed above, ongoing projects will all require Cultural Resource Protection and Preservation monitoring during construction in 2020. The UmaBirch Floodplain project and East Birch projects will be ongoing into the next CY.

Work Element D: 132. Produce (Annual) Progress Report
Work Element Title: Produce Annual Progress Report CY19 (Jan. 1, 2019, thru Dec. 31, 2019)
Milestone Deliverable: Completed annual report

A. Review progress report format requirements
B. Upload finalized RM&E technical report for BPA to publish
C. Distribute progress report for BPA review and comment
D. Upload non-technical progress report to Pisces
E. Review progress report format requirements
F. Draft CY2019 RM&E technical report
G. Interagency/tribal review
H. Confirm BPA posted received

The CY2019 BPA Annual Progress Report was completed and was uploaded to BPA through Pisces in the winter of 2020.

Work Element E: 114. Identify and Select Projects
Work Element Title: CTUIR Umatilla Subbasin Restoration Coordination
Milestone Deliverable: Develop or update prioritized Habitat Project list

CTUIR UBAFHP staff developed and annually updated habitat restoration and enhancement projects through coordination and planning with State, Federal and local partners, and private landowners consistent with the Subbasin Plan. This included participation with the UBWC and the Umatilla County SWCD. CTUIR completed a prioritized list of potential and final developed projects to be implemented contractually with BPA and other funding sources for the upcoming fiscal year and future year planning. Project development and planning were incorporated into this WE to assist in development of future funding packages.

Final Umatilla Willow Subbasin Plan (NPCC 2005),
Middle Columbia River Steelhead Recovery Plan (NMFS 2009),
Recovery Plan for the Coterminous United States Population of Bull Trout (*Salvelinus confluentus*) (USFWS 2015),
Meacham Creek Watershed Analysis and Action Plan (Andrus & Middel, 2003), and
Birch Creek Watershed Action Plan (CTUIR 2016).

Work Element F: 191. Watershed Coordination
Work Element Title: Umatilla River Watershed Coordination Duties
Milestone Deliverable: Coordinate Watershed Association Activities

A. Coordinate with Umatilla Basin Watershed Council
B. Coordinate with NRCS and local conservation districts
C. Network with professionals in the field of habitat restoration
D. Coordinate with co-manager ODFW and other Federal agencies

CTUIR UBAFHP staff participated and coordinated with multiple agencies and stakeholders in the Umatilla River Subbasin through the Umatilla Subbasin Restoration Team (Restoration Team), including ODFW, USDA-FS, NRCS, the Umatilla County SWCD, Umatilla Basin Watershed Council and local stakeholders to enhance natural resources, identify problems and solutions, coordinate efforts to prevent duplication, enhance communication and cooperation and identify funding and cost share opportunities within the Umatilla River Subbasin. Staff further coordinated with other agencies (e.g. USFWS, NOAA, EPA, BPA and etc.) in planning and implementing partner habitat restoration and enhancement projects, ESA planning processes, and project prioritization and selection processes. The Restoration Team was established in 2010 and is an informal group formed of agency or entity representatives that do restoration work within the Umatilla River /Willow Creek Basin floodplain and riverine system. The Restoration Team coordinated several passage projects in Birch Creek, and upcoming project activities in the lower Umatilla River. CTUIR staff prepared agreements, if necessary, to assign duties and responsibilities to the appropriate entities. We also developed documents, press releases, web sites, and other communications to impart information to participating stakeholders

and the public. Furthermore, CTUIR UBAFHP staff updated the Restoration Team, UBWC, CTUIR Committees and Commissions, and permitting agencies on project activities by presentation and in writing on project activities.

Work Element G: 99. Outreach and Education
Work Element Title: Public Outreach and Education
Milestone Deliverable: Complete Outreach and Education Activities

CTUIR UBAFHP staff educated the public on natural resource protection and restoration principles, and communicated on project activities throughout the year. This work included giving project tours and presentations (field, written, and verbal) and participating in local and regional workshops, symposia, technical teams and/or conferences (training, project presentation, and memberships), newspaper articles and public education (local school districts or college programs).

CTUIR UBAFHP staff completed CTUIR semi-annual reports summarizing project objectives and outputs, expected outcomes, and resulting impacts of project restoration activities (Figure 3). These reports are used by the CTUIR Department of Natural Resources to inform CTUIR staff and government officials, other agencies and entities, and the public of project activities.

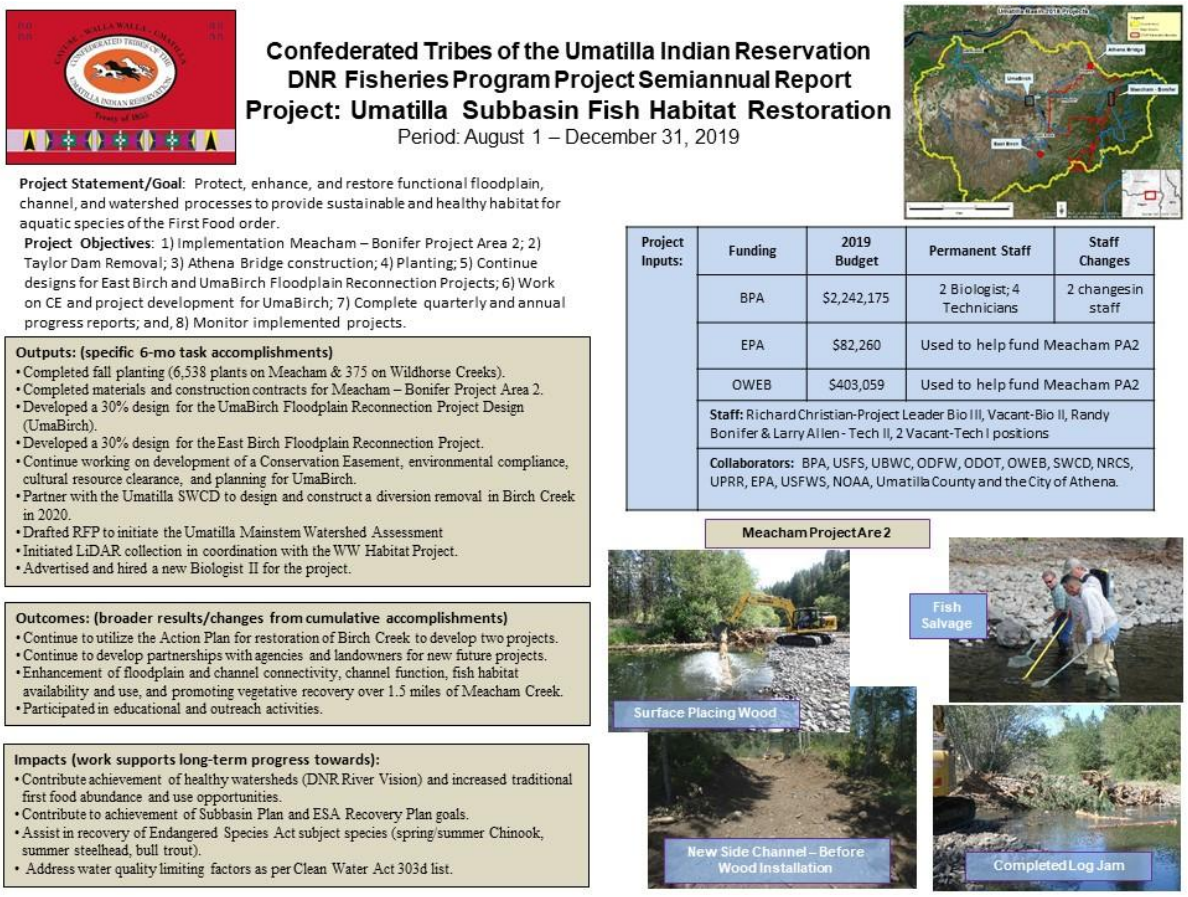


Figure 3. CTUIR semi-annual report for the Umatilla Subbasin Fish Habitat Restoration Project, August – December, 2019.

The UBAFHP participated in a number of community outreach and education opportunities in 2019. In March, 2019, the UBAFHP participated in a CTUIR Department of Natural Resources "open house." During this event, the UBAFHP educated the tribal community about the work that the Project recently completed and work that was upcoming in the recent months, including the Meacham Creek Bonifer Reach Floodplain Restoration and In-stream Enhancement Project. The UBAFHP again participated in the Watershed Field Days program to educate local elementary school children about the importance of stream and watershed health.

Numerous tours were also conducted of the previous work that has been completed on Meacham throughout the 2019 contract year. Some of these tours were for other resource professionals, while some of them were for educational purposes.





Figure 4. UBAFHP outreach and education activities. CTUIR community members learning about DNR projects at the annual open house (left); UPRR tour of Meacham Creek during high flows in April (right).

Project staff also developed and fostered relationships with participating experts in related fields by attending training, professional workshops and working groups, and gained professional advancement and improved project success through informative, instructional interactions. CTUIR UBAFHP and DNR Fisheries Habitat Program staff attended multiple professional conferences and workshops, and participated in poster presentations of project activities including:

River Restoration Northwest (2019 – Poster)
Ecological Response to Floodplain Reconnection and In-stream Habitat Enhancement –Richard Christian, Ethan Green, and Randy Bonifer.

Work Element H: 122. Provide Technical Review and Recommendation
Work Element Title: Review and Provide Technical Input on Issues and Topics that Affect the Areas Natural Resources
Milestone Deliverable: Provide Technical Input and Summaries to Enhance or Protect Natural Resources in the Subbasin

A. Conduct review and provide input as necessary on natural resource preservation issues.
B. Review and provide technical input on issues that may adversely affect natural resources.

CTUIR UBAFHP staff reviewed and provided technical input as applicable on plans and proposals by entities within the Umatilla River Basin that may adversely impact floodplain or riverine processes and biota productivity, public project planning relevant to floodplain, river and wetland restoration or impacts, development and review of grant funding proposals, and proposed landowner projects. Project staff provided input to multiple CTUIR departments on annual activities relevant to work within the floodplain, rivers, and wetlands, US Army Corps of Engineers/Oregon Division of

State Lands removal-fill permit applications, and CTUIR Stream Zone Alteration (SZA) Permit applications on work proposed within the floodplain on Reservation land.

Work Element I: 186. Operate and Maintain Habitat/Passage/Structure
Work Element Title: Inspect and Maintain Function of In-stream Improvement Structures
Milestone Deliverable: Maintain Proper Operation of In-stream Habitat Structures

A. Environmental compliance requirements complete.
B. The inspection, replacement and/or maintenance of passage and habitat structures.
C. Hire contractor to perform work.

CTUIR monitors 6 passage rectification projects to assure that treatments are effectively working and to insure that intrusive objects are not interfering with the designed function of the passage structures (Table 4). Routine quarterly scheduled site visits of individual projects are conducted either independently by the CTUIR or jointly with project partners such as ODFW. Site visits typically follow significant flow events or responses to landowner requests at project sites. Project maintenance included, but was not limited to, meeting specified conditional language in state and Federal permits, maintaining debris that is routinely captured or caught on in-stream structures, responses to landowner requests and concerns, and completion of post-treatment surveys to monitor and quantify changes to physical and ecological responses.

Work Element J: 186. Operate and Maintain Habitat/Passage/Structure
Work Element Title: Maintenance of Habitat Features Associated with Project Conservation Agreements
Milestone Deliverable: Maintenance of Land or Structures Associated with Conservation Agreements

A. Environmental compliance requirements complete.
B. Adhere to details of existing easements and/or initiate additional agreements as feasible.

The purpose of these Conservation Agreements is to protect, enhance, and restore functional floodplain, channel, and watershed processes to provide sustainable and healthy habitat for aquatic species in the Umatilla River subbasin. The UBAFHP have and will continue to maintain the individual projects to ensure that project structures and fencing are functioning and habitat recovery is progressing towards meeting projects goals and objectives. The CTUIR currently maintains 17 conservation agreements. Current agreements provide secured access and protection of resources for functional floodplain, channel watershed processes to provide sustainable and healthy habitat for aquatic specifies 26 miles of stream. CTUIR routinely conducts custodial maintenance on individual projects to ensure that project structures and fencing are functioning and habitat recovery is progressing towards meeting projects goals and objectives. Activities include, but are not limited to, installing and repairing riparian cattle exclusion fences, maintaining or installing water gaps, riparian and floodplain plantings and maintenance, noxious weed control, maintenance of fish habitat improvement structures, and landowner coordination and education.

Table 3. Habitat passage structures monitored and maintained by CTUIR to meet design specifications

Year	Stream	Stream Location	Project Description
2007	Meacham Creek	RM 1.7	Passage rectified by removing large cabled boulders (improved adult passage)
2007	Meacham Creek	RM 20.2	Partial dam removed (juvenile and adult passage)
2007	Camp Creek	RM 0.3	Partial dam removal (juvenile and adult passage)
2007	Greasewood Creek	RM 0.4	Partial dam removal (juvenile and adult passage)

2007	West Birch Creek	RM 3.2	Roughened channel to restore proper gradient and reduce step height at road bridge crossing for adult passage
2008	West Birch Creek	RM 2.7	Hoeft Dam fish passage rectification (juvenile and adult passage)
2019	Umatilla River	RM 48.2	Partial dam removed (juvenile and adult passage)
2019	Wildhorse Creek	RM 18.8	Passage rectified by removing concrete grade control structure and replacing bridge (juvenile and adult passage)

Work Element K: 198. Maintain Vegetation
Work Element Title: Maintain Vegetation and Control Noxious Weeds in Project Areas within the Umatilla River Subbasin
Milestone Deliverable: Maximize Survival of Native Vegetation in Enhancement Project Areas

A. Environmental compliance requirements complete.
B. Physical removal of non-preferred species of vegetative growth from project area.
C. Weed control in project areas by chemical means.
D. Water vegetation and reduce weed competition to improve survival at CTUIR project areas.
E. Till established weed areas as necessary for noxious weed control.

Project activities conducted in 2019 included the monitoring and maintenance of 17 conservation agreements on numerous individual landowner properties. Watering, weeding and maintenance methods for each Conservation Agreement and project area is important for enhanced native vegetation and project site but maintenance varies by site conditions. Strategies to address weeds are included in agreements that are either completed by the landowner, CTUIR, subcontractor, and/or through the County Weed Control Board. CTUIR staff provides assistance to landowners by coordinating and managing herbicide application, providing funding, and developing treatment strategies. Manual, biological and chemical treatment options are utilized by CTUIR and may be employed when consistent with existing standards. Weed control is essential in establishing native grass and plant species. The UBAFHP maintains a licensed pesticide applicator on staff to spray/control noxious weeds on sites where chemical application is necessary. This staff member identifies problem weeds, determines the appropriate herbicide and selects the most effective application methods and rates in accordance with the National Oceanic and Atmospheric Administration's (NOAA) Biological Opinion under BPA's Habitat Improvement Program. The UBAFHP utilizes backpack spraying applications to treat perennial, annual and biennial weed species. All herbicide applications are consistent with Oregon Revised Statue (ORS).570.505 and Federal Insecticide, Fungicide and Rodenticide Act (FIFRA) Regulations. CTUIR complies with BPA standards and supplies a report to BPA detailing the types and quantities of herbicides applied to specified locations.

In 2019 the UBAFHP completed 54.5 acres of mechanical and chemical weed treatment on current and completed project areas (Table 4).

Table 4. Noxious weed treatments completed by location within the Umatilla River Basin, 2019.

Stream Name	Latitude	Longitude	Acres Treated	Method	Species Targeted
Meacham Creek	45.6222	-118.35	12	Mechanical	*Potentilla recta, Centaurea* spp.
Wildhorse Creek	45.7483	-118.58	2	Chemical	*Conium maculatum*

	45.7483	-118.58	3	Mowing	*Conium maculatum*
Umatilla River	45.661	-118.99	37.5	Chemical	*Lepidium* spp., *Centaurea* spp.
	Total Acres Treated		54.5		

Work Element L: 184. Install Fish Passage Structure
Work Element Title: Wildhorse Creek – Athena Fish Passage Project Implementation
Milestone Deliverable: The CTUIR will work collaboratively with the ODFW, UBWC, City of Athena and Umatilla County to replace an aging bridge on 3rd Street in Athena, OR, to restore upstream fish passage through the project reach.

The CTUIR worked collaboratively with the ODFW, UBWC, City of Athena and Umatilla County to replace an aging concrete box structure on 3rd Street in Athena, OR. This allows for additional hydraulic freeboard at this site. In addition to the replacement, a roughened channel was constructed under the newly installed bridge to accommodate fish passage. The CTUIR has conducted radiotelemetry for adult steelhead in this stream, which identified this as a complete passage barrier to all life history stages. This project opened fish passage for 22 upstream miles. CTUIR worked collaboratively with the UBWC and in consultation with ODFW to implement the final designs that were developed to restore fish passage. The CTUIR planted 375 native riparian plants along the new roughened channel.



Figure 5: Athena Bridge Fish passage project before and after construction

Work Element M: 115. Produce Inventory or Assessment
Work Element Title: Produce Umatilla River Subbasin Assessment
Milestone Deliverable: Deliver a partial assessment including draft vision statement, draft objectives, data gaps, outline, and approach.

In this contract year, the CTUIR focused on identifying data gaps, developing an internal technical team, scoping the assessment, and weighing different approaches to the Umatilla River assessment. The UBAFHP worked closely with the CTUIR GIS department to identify existing data in the CTUIR repositories and in public databases as well as determining where critical data gaps exist. This information will be rolled into contract year 2020 where the UBAFHP will solicit proposals to begin composing the assessment document. In contract year 2019 the UBAFHP also continued coordinating with stakeholders including various tribal government departments, federal and state agencies, local governments, and local nonprofits to begin assembling a core technical team and several smaller teams to work on specific components of the assessment (e.g. Fisheries Committee).

Work Element N: 172. Conduct Pre-Acquisition Activities
Work Element Title: Conduct pre-acquisition activities for Birch Creek-Umatilla River confluence, UmaBirch LLC Properties
Milestone Deliverable: Produce the necessary documents and conduct surveys necessary to move forward with purchasing a conservation easement on the UmaBirch properties.

Significant coordination and planning efforts were accomplished in the 2019 contract year to advance this project to the execution of a conservation easement. The UBAFHP has been working closely with the landowner, other CTUIR projects, the UBWC, and Western Rivers Conservancy to determine the scope and terms of the easement, as well as the steps necessary to complete a conservation easement. Over the course of this contract year, the CTUIR held several coordination meetings to discuss next steps, coordinated with the landowner to consolidate ownership of several taxlots into a more manageable format for the easement, and initiated the process to produce a preliminary title report for the taxlots subject to the conservation easement. While progress was made, the deliverable for the Work Element was not fully met in this contract year. However, the landowner and the CTUIR are very motivated to complete the easement and the consolidation of ownership should facilitate further steps to be taken in contract year 2020. The conservation easement is anticipated to be completed in 2020.

Work Element O: 175. Produce Design and/or Specifications
Work Element Title: Reith Dam Removal Design and Permits
Milestone Deliverable: Complete a design and implementation schedule for one fish passage project on the mainstem Umatilla

CTUIR continued to work collaboratively with the landowners and BPA and in consultation with ODFW to develop the final designs and finalize all environmental compliance items on this project. The design, EC compliance and oversight was initiated during the previous CY and was finalized during this CY. BPA engineers provided engineering assistance to design this project and help with permitting. Please note that this project has been called a variety of different names, including: Wyss, Reith, Taylor and Brown's Dairy dam.

Work Element P: 84. Remove and/or Install Diversion
Work Element Title: Reith Dam Removal Implementations
Milestone Deliverable: Work collaboratively with the ODFW, UBWC, and Umatilla County to remove an irrigation diversion on the mainstem Umatilla River, near Reith, OR

The CTUIR worked collaboratively with the ODFW, UBWC, and Umatilla County to remove an irrigation diversion on the mainstem Umatilla River, near Reith, OR. The concrete irrigation dam that spanned the entire channel hindered fish passage. The CTUIR solicited bids and selected a contractor in cooperation with the other stakeholders previously mentioned. An open, fair, competitive bid process was used to select a construction company on this project. EC compliance began during the last CY and was completed in this CY prior to implementation. BPA provided engineering support for completing topographic surveys, the development of the surface layer, habitat analysis, hydraulic model development and report, geomorphic assessment, development of the restoration design alternatives analysis, development of the implementation plan and schedule, and permitting.

During design and implementation, this project area had many names. In the beginning, Brown's Dairy Dam was the given name. Landowner clarifications led the name change to Taylor Dam. As there are other Taylor Diversion projects, CTUIR and collaborators settled on Reith Dam to be used on cbfish and any future documents.







Figure 6: Umatilla River at the Reith Dam site, before, during, and after construction

Work Element Q: 175. Produce Design and/or Specifications
Work Element Title: UmaBirch Properties – Floodplain Restoration and Habitat Enhancement Design
Milestone Deliverable: Produce designs and constructible implementation plans for several phases of restoration work on the UmaBirch easement property.

In 2019, UAFHP staff continued to create a design and develop a formal conservation easement for restoration work on the UmaBirch easement property project established in 2017. The 30% design completed in 2019 identified actions taken to increase habitat and floodplain function and design them to a constructible implementation plan. The design will continue to be developed in close collaboration with the landowner, who has shown great interest in conservation and restoration on their property. Given the large scale of the project site, the designs will likely be designed for implementation in phases, with each phase consisting of work feasible to complete in a single year. Phasing designs allows the CTUIR to be flexible in its restoration strategy at the site and plan projects for out years more easily.

Work Element R: 29. Increase Aquatic and/or Floodplain Complexity
Work Element Title: Construction – Bonifer Floodplain Restoration and In-stream Enhancement – PA 2
Milestone Deliverable: Complete installation of 75 unanchored log structures, 50 boulders, and install 26 engineered log jams.

CTUIR subcontracted construction services to complete installation of large wood structures in the Meacham Creek Bonifer Reach Project Areas. This project area involved 0.95 linear miles of Meacham Creek, with the installation 243 pieces of large wood, including 45 individual log structures, 24 engineered log jams, and 125 boulder structures.

Work Element S: 30. Realign, Connect, and/or Create Channel
Work Element Title: Construction – Bonifer Floodplain Restoration and In-stream Enhancement – PA 2
Milestone Deliverable: Complete 2,250 feet of secondary channel excavation; installation of 198 logs (180 with root wads; 18 without root wads).

CTUIR subcontracted construction services to complete construction of primary and secondary pilot channels in the Meacham Creek Bonifer Reach Project Area 2 as part of the Bonifer Reach Floodplain Reconnection and In-Stream Enhancement Project. CTUIR was able to excavate 2640 feet of side channel in order to construct 7656 feet of new channel. 243 logs were installed; 225 with root wads, 18 without root wads.

2018	2019
	



Figure 7. Before (2018) and after (2019) photos of the Meacham Creek Floodplain Restoration and In-stream Enhancement Project Area 2 taken at photo point monitoring locations.

Table 5. Meacham Creek Bonifer Reach implementation schedule.

Implementation Year	Project Areas	Stream Location	Project Description
2017-18	3 & 4	RM 4.05 – 5.7	Remove levees/dikes, create primary and secondary channel, enhance pool/alcove habitat, construct large woody jams, add large wood, construct embankments
2019	2	RM 3.25 – 4.05	Create primary and secondary channel, add large wood
2020	1 & 5	RM 1.9 – 3.25, Bonifer Pond	Reconnect Bonifer Pond to Boston Canyon Creek, remove levees/dikes, create side channel, add large wood, construct embankments

Work Element T: 47. Plant Vegetation
Work Element Title: Meacham Creek Floodplain Restoration and In-Stream Enhancement, RM's 3.2-6.1 Planting
Milestone Deliverable: Complete Scheduled Tree and Shrub Plantings in Project Areas

A. Environmental compliance requirements complete.
B. Agreement with the Native Plant Nursery for Growing Plants and Developing Plant Protocol.
C. Establish Planting Locations in Existing Project Areas for Increased Recovery.

UBAFHP staff annually plant vegetation and distribute native grass seed in areas we have implemented existing or new habitat enhancement projects or have identified a need in maintained riparian Conservation Agreement areas. In 2019, the UBAFHP completed a fall planting effort within the previously implemented Meacham Creek Floodplain Restoration and In-stream Enhancement Project. The fall 2019 planting effort included installing 6956 containerized, native plants in Meacham Creek.

Planting tasks include site planning and development of planting strategies, collection and preparation of materials (pruning and conditioning of live willow material), pre-order coordination with the CTUIR Tribal Native Plant Nursery, and installation. Planting techniques are customized for conditions within each project area. Planting location, species, age, form (cuttings, saplings, bare-roots, potted, plugs), and soil/substrate conditions were considered and addressed during the implementation planning phase. The CTUIR UBAFHP staff work closely with the Tribal Native Plant Nursery to collect local seed and plant stock to provide native plants for particular project areas by elevation and planting zones.



Figure 8: CTUIR planting native vegetation at the Meacham Creek Project Site (Left) and the Athena Bridge Passage Project at Wildhorse Creek (Right).

Work Element U: 175. Produce Design and/or Specifications
Work Element Title: East Birch Creek RM 5.3 – 5.8 Habitat Enhancement Project Design
Milestone Deliverable: Complete a design and implementation plan for a floodplain reconnection and habitat enhancement project.

In this contract year, the UBAFHP worked closely with the selected engineering firm and the landowner to determine project elements and a more detailed footprint that would both satisfy the needs of the landowner and provide the fisheries uplift required for the UBAFHP. A 15% design was produced in contract year 2018, which led to additional

concerns from the landowner and further discussions. The UBAFHP consulted with the BPA RRT for guidance on what quantity of fisheries benefit would be required for continued funding and consideration. After going through several rounds of comments with RRT, the UBAFHP and the landowner decided to move forward to a 30% and 60% design, revisit the recommendations from RRT, and determine if it is acceptable for the landowner to feel comfortable moving forward with the project. The design and implementation plan is anticipated to be completed in contract year 2020.

Work Element V: 29. Increase Aquatic and/or Floodplain Complexity
Work Element Title: Construction – East Birch Creek Floodplain Reconnection
Milestone Deliverable: Complete installation of 15 logjam structures and 85 boulder structures to increase floodplain complexity.

Under the previous contract, a design was initiated to reconnect the floodplain through this 0.8 mile reach. As mentioned in Work Element U, this project is still in the design stage. A completely new RRT in 2019 required increased engagement and slower progress to ensure that all parties were properly informed on the project and comfortable moving forward. Implementation is expected to begin in contract year 2020, with the design and implementation plan anticipated to be completed in early 2020. There were some discussions about potentially buying the property from the current owner. This will be fully explored during the next contract period, as it would change the project parameters.

Work Element W: 30. Realign, Connect, and/or Create Channel
Work Element Title: Construction – East Birch Creek Floodplain Reconnection
Milestone Deliverable: Completed channel construction.

Under the previous contract, a design was initiated to reconnect the floodplain through this 0.8 mile reach. As mentioned in Work Element U, this project is still in the design stage. A completely new RRT in 2019 required increased engagement and slower progress to ensure that all parties were properly informed on the project and comfortable moving forward. Implementation is expected to begin in contract year 2020, with the design and implementation plan anticipated to be completed in early 2020.

Work Element X: 29. Increase Aquatic and/or Floodplain Complexity
Work Element Title: Install Wildhorse Creek Beaver Dam Support Structure
Milestone Deliverable: Work cooperatively with the SWCD to install 8 beaver dam support structures

Due to complications with ODFW Fish Passage Permitting, UBAFHP staff were unable to install beaver dam support structures. Instead, small logs were placed in the active channel as brush mats.





Figure 9: Original plan for beaver dam analog installation (left). Installation of tree brush mats (right).

Work Element Y: 115. Produce Inventory or Assessment
Work Element Title: New CCR 43149 Upper Umatilla River LiDAR Aquisistion
Milestone Deliverable: Summarized aquatic, physical habitat, and water quality data.

A. Environmental compliance requirements complete.
B. Environmental conditions
C. Interpretation and synthesis
D. Incorporate project effectiveness and regional data into project activities and annual BPA report

UBAFHP staff collected and maintained field data necessary to inform project tasks and habitat site management in 2019. Data collected included vegetation surveys from 34 previously and newly established transects in past planting sites to determine site survival, natural regeneration, as well as to survey for any noxious weeds that may require control.

Concurrently with vegetation transects, previously planted areas were surveyed for invasive weed species. Eleven major weed species were identified in the Meacham Creek Floodplain Restoration and In-stream Enhancement project area in 2018. The most abundant weed species found was Viper's bugloss (*Echinum vulgare*) and the highest priority species for control identified was invasive blackberry (*Rubus* spp.; Table 3).

Table 6. Invasive weed species detected in Meacham Creek Floodplain Restoration and In-stream Enhancement Phase I and II planting areas in 2016 and relative priority for control efforts.

Species Common Name	Species Scientific Name	Priority	Frequency (# of sites present
Diffuse knapweed	*Centaurea diffusa*	High	6
Spotted knapweed	*Centaurea stoebe*	High	7
Eurasian blackberries	*Rubus* spp.	High	12
Sulfur cinquefoil	*Potentilla recta*	High	3
Yellow starthistle	*Centaurea solstitialis*	High	1
Bull thistle	*Cirsium vulgare*	Moderate	2
Multiflora rose	*Rosa multiflora*	Moderate	2
St. John's wart	*Hypericum perforatum*	Moderate	3
Viper's bugloss	*Echinum vulgare*	Moderate	13
Wild carrot	*Daucus carota*	Moderate	1
Curly dock	*Rumex crispus*	Low	3

The CTUIR UBAFHP also continued its intensive photo point monitoring in the 2019 contract year. Photo points captures were conducted in the spring of 2018 and fall of 2019 and uploaded to the UBAFHP internal photo point data depository (Figure 12).

Work Element Z: 100. Construction Management
Work Element Title: [CCR-43748]: Site Preparation, Materials Management, Field Engineering, Quality Assurance, Construction Oversight: Birch Creek (RM-2.3)
Milestone Deliverable: Construction Management Complete

A. Collect and review daily construction logs
B. Review /approve change order requests on any desired change orders before directing the construction contractor to make them
C. Review subcontractor's requests for payments

This work element will be moved to a new contract during the 2020 CY. During discussions with BPA, it was determined that this would be a more efficient contracting mechanism.

Discussion

The projects implemented in this reporting period were carefully designed in previous years to mitigate for the identified ecological concerns and align with local assessments. The CTUIR approaches restoration utilizing the Umatilla River Vision, previously described (Jones et al. 2008). The process-based philosophy of the River Vision encourages development of projects that address multiple River Vision Touchstones, limiting factors, and ecological concerns (Table 9).

Table 7. The Umatilla Anadromous Fish Habitat Project objectives relative to the Umatilla River Vision touchstones (Jones et al. 2008), BPA 2008 Fish Accords primary limiting factors (Fish Accords 2008) and NOAA's ecological concerns (NMFS 2009).

Umatilla Habitat Program Objectives	Umatilla River Vision 2008 Touchstones Addressed	BPA 2008 Fish Accords Primary Limiting Factor's Addressed	NOAA Ecological Concerns	NOAA Ecological Concerns Subcategories
Protect and conserve natural ecological processes that support the viability of fish populations and their primary life history strategies	Biota Connectivity Geomorphology Hydrology Riparian Vegetation	In-channel Characteristics Floodplain/Riparian Sediment	Multiple(Habitat Quantity, Injury and Mortality, Peripheral and Transitional Habitats, Channel Structure and Form, Sediment Conditions, Water Quality, Water Quantity, Population Level Effects)	Multiple
Restore passage and connectivity to habitats blocked or impaired by artificial barriers and maintain properly function passage and connectivity	Geomorphology Connectivity	Passage/Entrainment	Habitat Quantity	Anthropogenic Barriers
Maintain and restore floodplain connectivity and function	Aquatic Biota, Connectivity, Riparian Vegetation, Geomorphology, Hydrology	Water Quality-Temperature Riparian/Floodplain	Food, Peripheral and Transitional habitats, Riparian Condition, Channel Structure and Form, Water Quantity	Altered Primary Productivity, Altered Prey Species Composition and Diversity, Riparian Condition, LWD Recruitment, Floodplain Condition, Bed and Channel Form, Instream Complexity, Decreased Water Quantity, Altered Flow Timing
Restore degraded and maintain properly function channel structure and complexity	Connectivity, Riparian Vegetation, Geomorphology	In-channel Characteristics	Riparian Condition, Peripheral and Transitional Habitats, Channel Structure and Form	Riparian Condition, LWD Recruitment, Side Channel Conditions, Floodplain Condition, Bed and Channel Form, Instream Structural Complexity
Restore riparian condition and LWD recruitment and maintain properly functioning conditions	Aquatic Biota, Riparian Vegetation, Hydrology	In-channel Characteristics Riparain/Floodplain	Food, Riparian Condition	Riparian Condition, LWD Recruitment, Altered Primary Productivity, Food-Competition, Altered Prey Species Composition and Diversity
Restore natural hydrograph to provide sufficient flow during critical periods	Connectivity, Aquatic Biota, Hydrology,	Floodplain/Riparian Water Quality-Temperature	Habitat Quantity, Water Quality, Water Quantity	HQ-Competition, Oxygen, Increased Water , Alter Flow Timing
Improve degraded water quality and maintain unimpaired water quality	Hydrology, Aquatic Biota	Floodplain/Riparian Water Quality-Temperature	Riparian Condition, Sediment Conditions, Water Quality	Riparian Condition, Decreased Sediment Quantity, Temperature, Oxygen Turbidity, Toxic Contaminants

Habitat protection and restoration actions, like those completed during this review period, were identified in numerous local assessments and planning documents. The Umatilla River Basin TMDL and WQMP (ODEQ and CTUIR 2001), Umatilla/Willow Subbasin Plan (NPCC 2005), Middle Columbia Steelhead DPS ESA Recovery Plan (2009), and the Recovery Plan for the Coterminous United States Population of Bull Trout (USFWS 2015) all identify one or more habitat

restoration or protection actions implemented by the UBAFHP in this reporting period as a way to address issues facing ESA-listed fish species and/or water quality concerns. In addition to the subbasin-scale planning documents, the restoration activities completed by the UBAFHP in this reporting period are also supported by several smaller scale watershed assessments. The Meacham Creek Watershed Analysis and Action Plan (Andrus and Middel 2003) and the Birch Creek Watershed Action Plan (CTUIR 2016) both specifically support the restoration actions completed in those watersheds.

LESSONS LEARNED AND ADAPTIVE MANAGEMENT

Lessons Learned

During this reporting period, the UBAFHP completed work in areas with multiple jurisdictions, subcontracted several large design and construction contracts, and maintained complex partnerships with landowners and local action agencies. The wide variety of work presented a number of unique challenges. As a result of working through these challenges, the UBAFHP has learned several lessons that will inform future project work.

Several of the projects in this reporting period included working closely with agency partners and participating landowners. Cultivating these partnerships has led to rewarding outcomes, as well as occasionally limiting progress on project work. One of the successes in this project period that required close coordination with agency and landowner stakeholders in the basin was the completed removal of the Reith Dam on the mainstem Umatilla River. The UBAFHP worked with the subbasin co-managers at ODFW, the UBWC, and surrounding landowners to complete the project. This complex project required leveraging the strengths of the different stakeholders and strategically targeting funding sources for different components of the project as a whole. By collaborating and working as a restoration team, a longstanding barrier was removed from the Umatilla River.

Conversely, not all of the collaborative projects proposed in this reporting period have gone exactly as planned. There were some partner issues during the implementation of the Wildhorse Creek – Athena Fish Passage Project. While the roles of each organization were identified at the outset of the partnership, communications were not maintained adequately during the project. In the future, the UBAFHP will clearly identify project goals and timelines to potential partner organizations at the beginning of projects and maintain coordination throughout to ensure all parties complete their assigned tasks.

Another issue that was unable to be overcome during this contract year related to the beaver dam support structure pilot project. The UBAFHP completed ESA consultation and designed the project, but the final fish passage approval was never obtained from the ODFW Fish Passage Coordinator. UBAFHP staff tried repeatedly to communicate with the Coordinator. At this time it isn't clear how this can be overcome in the future.

In a similar vein, the UBAFHP also faced some challenges with landowner partnerships on some projects. The UBAFHP has been developing and designing a floodplain reconnection project on East Birch Creek on a private landowner's property. The CTUIR and the landowner entered into an agreement to pursue a mutually-beneficial project, but there have been differences in stakeholder priorities since the design began in CY2018. Design firm and UBAFHP staff have been attempting to balance floodplain connection, fisheries benefit, and the concerns of the landowner and the time and effort put into landowner engagement and negotiation has led to the design being delayed. At present, the design is proceeding to a 60% design of the preferred alternative with the understanding that the landowner and CTUIR will agree to the project footprint and general project elements at that stage and continue with the design. Implementation is set to begin in 2020. In the future, the UBAFHP will make an effort to complete more landowner education when entering into a partnership, as well as clearly define the goals of all groups as well as the timeline for the project and relevant deadlines.

Increased engagement with a completely new staffed RRT also played a role in the delay of project designs for East Birch and Umabirch. Due to everyone on the team being new to the project, they required significant involvement to become familiar with the project. In 2020, UBAFHP hopes to create a manageable and efficient communication plan with the RRT to ensure effective design processes in the future.

Adaptive Management

The UBAFHP places a heavy weight on adaptive management, applying lessons learned in past years, and using research and action effectiveness monitoring data to support project decision making.

Lessons learned identified in previous year's annual reports play a large part in the management of habitat restoration site and the development of future projects. For example, in the CY2016 annual report, we identified recommendations for increasing planting survival and increasing revegetation success following restoration projects. In this reporting period, the UBAFHP has incorporated those recommendations into the annual planting plan. For example, the CTUIR has adopted a planting methodology that prioritizes immediate planting of wetland and riparian areas and letting heavily disturbed upland/floodplain areas settle for two years prior to planting containerized plants. The plant mix that UBAFHP staff planted was also much more targeted to the microsites available in the planting locations, ensuring that more hydrophilic species are planted in the most sensitive sites. The UBAFHP continues to improve the species mix based on ecological suitability and enhancement of First Foods species. Similarly, all plantings were completed in fall, taking advantage of a longer dormancy window in the plants and allowing containerized plant's roots to infiltrate the soil early and quickly in the spring and take advantage of seasonally high groundwater elevations.

The UBAFHP also kept revegetation in mind during implementation. Based on observed conditions in previous year's projects, projects completed in this reporting period included enhanced floodplain topography creation to help increase plating survival and natural vegetative regeneration. In any area of disturbed floodplain encountered in UBAFHP project areas (e.g. the floodplain surface following a levee removal), 2-5 foot deep depressions were excavated to mimic natural floodplain features such as relic channels. Excavating these depressions allows groundwater to be nearer to the ground surface, becoming more available to young plants. Additionally, the floodplain topography creates microsites that collect floodwaters and precipitation and provide cover from insolation and wind that may help plants naturally establish and become a seed source and additional cover for other plants.

The UBAFHP also incorporated lessons learned in past years into project development and implementation methodology. During the design process for the Meacham Creek Bonifer Reach Floodplain Reconnection and In-stream Enhancement project, the UBAFHP and the design firm engaged in a lessons learned exercise to improve the design process from the Meacham Creek Phase I and Phase II projects. One of the recommendations of this exercise was to make more efficient and judicious use of large woody material. This recommendation was also supported by CTUIR biomonitoring reporting that concluded that most of the large wood installed in previous project was not in contact with the water during summer baseflow. During this reporting period, staff made a concerted effort to place individual pieces of large wood directly in contact with baseflow and "seed" the upper end of the project area with unanchored pieces of wood in the anticipation of the creek self-sorting wood into more natural aggregations.

In addition to the lessons learned from previous project years, project staff also incorporate data collected by other CTUIR projects and from annual project data inventories of previously implemented projects. The UBAFHP annually inventories plant survival and revegetation progress, as well as noxious weed presence and extent of infestations. The UBAFHP is responsible for treating noxious weeds on several hundred acres of project areas and staffing and time constraints mean that treatment areas and species must be prioritized in order to achieve project objectives of promoting native plant growth in project areas. The UBAFHP sets priorities and manages conservation agreement properties using a rich dataset collected by project staff as well as incorporating data from the Oregon Department of Agriculture, USDA-FS, and Umatilla County Public Works. Using this dataset, the UBAFHP is able to identify the highest priority weeds in priority areas, direct staff time to the most important areas, and apply the least invasive and most ecologically benign treatment while remaining effective.

The UBAFHP also integrates data collected from research, monitoring, and evaluation efforts by the CTUIR and ODFW to inform future project development. Monitoring of outmigrating steelhead smolt survival from the Meacham Creek and Birch Creek screw traps to Three Mile Dam suggest that the mainstem Umatilla River is a source of significant mortality. Survival rates between Meacham Creek and Three Mile Dam have been recorded as low as 22% (Contor et al. 2016). Recognizing that many of the juvenile salmonids currently being produced in the system are not successfully migrating to the mainstem Columbia River and the Pacific Ocean beyond, the UBAFHP has begun planning more habitat improvements in the mainstem Umatilla River. The objective is to improve habitat conditions in the mainstem Umatilla River to provide outmigrating smolts habitat to rear over winter, refuge from high flow events, cover from predators, and increased water quality.

SUMMARY AND CONCLUSIONS

In accordance with the 2006 NPCC solicitation outline, the CTUIR UBAFHP since 2007 focused its restoration activities primarily on Meacham Creek, Birch Creek, and mainstem Umatilla River. However, project restoration activities occur in other areas of the basin where floodplain and riverine processes are treated with outcomes that are beneficial to ecological processes, water quality and fish production. The Meacham Creek Watershed has long been a primary focal point of the CTUIR effort to improve habitat conditions in the Umatilla Basin because of its location, size, historical significance, and recovery potential. **Error! Reference source not found.** highlights the CTUIR Umatilla Anadromous Fish Habitat Project restoration accomplishments since 2007.

Proposed restoration actions have focused on protection, enhancement, and restoration of functional floodplain, channel and watershed processes at multiple scales using passive and active restoration techniques. Over the past decade, the CTUIR Department of Natural Resources and UBAFHP have transitioned from restoration toward a fixed endpoint to address symptoms to a restoration of processes. Restoration of process is more likely to address causes of river ecosystem degradation, whereas restoration toward a fixed endpoint addresses only symptoms. Specific restoration actions proposed for completion by CTUIR, partnering agencies and hired independent contractors include levee and dike removal and or modification, floodplain and channel construction, in-stream and floodplain large wood debris additions, in-stream structure placement, wetland enhancement, floodplain and riparian plantings, noxious weed removal, riparian management through fencing, and removal of physical migration barriers. The UBAFHP have and will continue to maintain project areas under secured conservation agreements with landowners on private properties for protection and enhancement of floodplain and riparian habitat and investments from past passage and in-stream structure projects. Completed project activities are described below in more detail in the context of the watershed with reference to annual progress reports.

During this reporting period, the UBAFHP continued to implement habitat improvement projects at a high level. The Reith Dam Removal was a long-discussed project in the subbasin that had never been implemented in the past. The CTUIR UBAFHP was able to work with agency partners and private stakeholders to implement the removal and rectify a partial barrier to upstream salmonid migration that had been recognized as a significant issue in the subbasin. The UBAFHP was also able to complete 0.95 miles of floodplain reconnection and in-stream enhancement in the Meacham Creek Bonifer Reach. The project included new channel construction, relic channel reconnection, and large wood addition that will “jumpstart” natural floodplain processes and set the reach on a recovery trajectory. UBAFHP also completed rectification of a fish passage barrier at the 3rd Street Bridge in Athena, Oregon. This project was crucial to reconnect over 24 kilometers of potential spawning habitat for Middle Columbia River Steelhead. In addition to project implementation, UBAFHP staff completed maintenance of ongoing riparian enhancement and passage projects at properties where the CTUIR has pre-existing riparian conservation agreements. This maintenance included noxious weed treatment, maintenance of built structures, and additional riparian plantings as needed.

The CTUIR UBAFHP made great progress on several design documents that will serve to inform projects in the long and near term future of the UBAFHP. The UBAFHP produced a preliminary design for a floodplain reconnection and in-stream enhancement project on East Birch Creek. This project is a direct result of the Birch Creek Watershed Action Plan process and is an important first step in the watershed.

A principal strength and focus of the CTUIR UBAFHP project is the ability to work cooperatively with the various entities throughout the restoration process. Staff participated and cooperated with multiple agencies and stakeholders in the Umatilla Basin Watershed including ODFW, USDA-FS, Natural Resource Conservation Service, Umatilla Basin Watershed Council, Umatilla County Soil and Water Conservation District, and local stakeholders to enhance or protect natural resources, identify problems and solutions, coordinate efforts to prevent duplication, enhance communication and cooperation and identify funding and cost share opportunities within the Umatilla River Subbasin.

The Umatilla Basin Anadromous Fisheries Habitat Project is an ongoing effort to protect, enhance and restore functional floodplain, channel and watershed processes to provide sustainable and healthy habitat for aquatic species in the Umatilla River Basin, including Threatened Middle Columbia River Steelhead. Project work further supports the CTUIR Department of Natural Resource River Vision and First Foods mission statements to sustain production. The River Vision principles have been successfully applied in effort to reestablish the salmonids to self-sustaining levels. We expect a substantial positive response of salmonid populations once habitat floodplain and channel function is addressed and improved. We believe a positive correlation between habitat improvement, salmonid density, and fitness levels will shift the status of ESA-Listed species towards a safer level of sustainability in the Umatilla River Basin

Table 8. The CTUIR UBAFHP restoration project descriptions by location, treated primary limiting factors (NMFS 2009) by CTUIR River Vision touchstones (Jones et al. 2008) and accomplishments; 2007-2019.

Subbasin, Stream and Years	Project Description	Species	CTUIR River Vision Touchstones/ Habitat Limiting Factors (PLF's shaded in yellow-NOAA BiOP)								Comment/ Accomplishments
			Biota-Connectivity	Geomorphology	Connectivity		Hydrology			Riparian Vegetation	
			Passage Barriers/ Entrainment	In-channel Characteristics	Habitat Diversity (LWD)	Floodplain Confinement	High Temps	High Turbidity	Low Flows	Riparian/ Floodplain	
Meacham Creek and Camp Creek, Tributary of Meacham Creek (2007)	Fish passage rectifications, pool development with rock structures, and plantings	STS	**X**				**X**			**X**	Rectified two diversion dams and one in-stream structure providing unimpeded access to the entire watershed, development of pools with boulder cross vanes, 335 ft of streambank stabilization with added wood complexity, 0.3 miles livestock exclusion fence, and 500 riparian plantings.
West Birch Creek (2007-2008)	Fish passage rectification, riparian protection fencing and plantings	STS	**X**		**X**		**X**			**X**	Rectification of the Cunningham and Hoeft Dams providing 2.4 miles unimpeded habitat, 335 ft of streambank stabilization with added wood complexity, 0.3 miles livestock exclusion fence, and 5,000 riparian plants.

Mainstem Umatilla River (Initiated 2008-2012)	Treated and maintained 3.5 miles of floodplain and channel; riparian and uplands	CHS, CHF, STS, Coho			X		X	X	X	X	Conservation Agreement on B&G Property to maintain 355 (61 riparian and 294 upland acres; installation of 60.7 acres of CREP tract's), 2 off-channel water wells, 13,400 seedling trees planted, 1,335 lbs of native grass seed and noxious weed control; Installation of an access restriction fence (3 additional riparian acres protected).
Meacham Creek (2009)	Floodplain improvement with levee setback, initiation of off-channel rearing habitat, large wood placement, and riparian plantings	CHS, STS,BT, Pacific Lamprey	X	X	X	X	X		X	X	Restored 40 acres of floodplain connectivity over 1-mile of stream by removal or modification of 3 levees and 1 dike (3,200 linear ft, 24,000 cubic yards); distribution of large wood on floodplain; 15,000 planted hardwood and conifer seedlings (30acres).
Meacham Creek (Initiated 2008-2012)	Riparian protection fencing and plantings	CHS, STS,BT, Pacific Lamprey		X	X		X		X	X	Built 9.8 miles of livestock exclusion fence between RM 2.0-8.5 (~350 acres protected).
Birch Creek (2010-2016)	Bank stabilization and large wood habitat complexity and riparian plantings	STS		X	X	X	X	X		X	Restoration of 335 ft of streambank stabilization with large wood and boulders over 0.1 miles of stream, 2 large wood in-channel habitat structures, and planted 5,000 riparian plantings over the 1-mile property.

Meacham Creek Floodplain Restoration and In-Stream Enhancement Phase I Project RM 6-7.1 (2011-2012)	Floodplain and channel improvement with levee setback, large wood placement, side-channel connectivity, wetland enhancement, and riparian plantings.	STS, CHS, BT, Pacific Lamprey		X	X	X	X	X	X	X	Reconnected 67 acres of floodplain over 1-mile of stream by removing a 2,800 foot levee and modification of two spur dikes (600 ft removed), realigned historic channel with meanders in the floodplain, developed 3 secondary channels and 3,568 ft of off-channel habitat, 12 large pool structures, 10 major and 286 medium rock and log features, and installed 38,290 plantings.
Birch Creek (2012)	Fish passage rectification and habitat restoration project.	STS, Coho	X	X		X	X	X		X	Removed two abandoned irrigation diversions (Taylor Property-ODFW lead agency) providing unimpeded access to 2.7 river miles of stream. Included channel reshaping, setback of leveed road adjacent to the channel; and reshaping of the channel and banks, two j-hook rock structure placements and riparian plantings over 0.6 miles of stream.
West Birch Creek (2012)	Fish passage rectification and habitat	STS	X	X	X		X	X		X	Removed one abandoned irrigation diversion (Low Property-ODFW lead

	restoration project.										agency) providing unimpeded access to 5.0 river miles of stream, installation of rock and large wood structures, channel re-shaping and plantings over 1-mile of stream.
Dillon Diversion Dam Removal (2017)	Fish passage rectification	STS, CHS, CHF, Coho, BT, Pacific Lamprey	X	X							Removed a longstanding partial barrier to upstream migration and opened an additional 3.65 miles of river to unimpeded travel for anadromous salmonids.
Meacham Creek Bonifer Reach Floodplain Reconnection and In-stream Enhancement – Project Areas 3 & 4 (2017-2018)	Floodplain and channel improvement with levee removal, channel reconnection, large wood placement, and riparian plantings	STS, CHS, BT, Pacific Lamprey		X	X	X	X	X	X	X	Treated over 1.6 miles of Meacham Creek by removing 3,385 linear feet of levees and dikes, reconnecting 3,766 linear feet of primary and secondary channel habitat, and installing 69 engineered log jams with more than 537 logs with rootwads attached.
Basin-wide easements O&M (2008-2018)	Ongoing maintenance of 17 riparian conservation agreements including livestock exclusion fencing, tree planting and weed control	CHS, CHF, STS, Coho, BT, Pacific Lamprey	X	X	X	X	X	X	X	X	552 acres protected and maintained, 15.15 miles of riparian fence protection (184 ac.), 7,300 planted hardwood seedling trees.
Meacham Creek Bonifer Reach Floodplain Reconnection and In-stream Enhancement –	Floodplain and channel improvement with channel creation and reconnection,	STS, CHS, BT, Pacific Lamprey		x	x	x	x	x	x	x	Treated 0.95 miles of Meacham Creek by creating and reconnecting 7,656 feet of primary and secondary channel

Project Area 2 (2019)	large wood placement, and riparian plantings										habitat, and installing 14 engineered logjams, 45 individual log structures, and 130 boulders
Reith Dam Removal (2019)	Fish passage rectification	STS, CHS, CHF, Coho, BT, Pacific Lamprey	**X**	**X**							Removed a longstanding partial barrier to upstream migration and opened miles of river to unimpeded travel for anadromous salmonids.
Athena Bridge Fish Passage Project (2019)	Fish passage rectification	STS, BT, Pacific Lamprey	**X**	**X**						**X**	Removed fish passage barrier, replaced bridge, placed rock structures and planted native riparian vegetation.

LITERATURE CITED

Alt, D. and D.W. Hyndman 1995. *Northwest Exposures: A Geologic Story of the Northwest*. Mountain Press Publishing Company, Missoula, MT.

Andrus, C. & J. Middel 2003. Meacham Creek Watershed Analysis and Action Plan; Final Report. pp. 125, Prepared for the Confederated Tribes of the Umatilla Indian Reservation.

Arrigoni, A.S., Alicia S., Poole, G.C., Mertes, L.A.K., O'Daniel, S.J., Woessner, W.W., Thomas, S.A. 2008. Buffered, lagged, or cooled? Disentangling hyporheic influences on temperature cycles in stream channels. WATER RESOURCES RESEARCH, VOL. 44, W09418, 13 PP

Arscott, D. B., K. Tockner, and J. V. Ward. 2000. Aquatic habitat diversity along the corridor of an alpine floodplain river (the Fiume Tagliamento, Italy). Archiv Fur Hydrobiologie 149:679-704.

Arscott, D. B., K. Tockner, and J. V. Ward. 2001. Thermal heterogeneity along a braided floodplain river (Tagliamento River, northeastern Italy). Canadian Journal of Fisheries and Aquatic Sciences 58:2359-2373.

Baxter, C. V., and Hauer, F. R. 2000. Geomorphology, hyporheic exchange, and selection of spawning habitat by bull trout (Salvelinus confluentus): Canadian Journal of Fisheries and Aquatic Sciences 57:1470-1481.

Beechie, T., and Bolton, S., 1999. An approach to restoring salmonid habitat-forming processes in Pacific Northwest watersheds: Fisheries 24:6-15.

Beechie, T.J., G. R. Pess, P. Roni, G. Giannico. 2008. Setting river restoration priorities: a review of approaches and a general protocol for identifying and prioritizing actions. North American Journal of Fisheries Management 28:891-905.

Beechie, T.J., Sear, D.A., Olden, J.D., Pess, G.R., Buffington, J.M., Moir, H., Roni, P., and Pollock, M.M., 2010, Process-based principles for restoring river ecosystems: Bioscience, v. 60, p. 209-222.

Bencala, K.E., and Walters, R.A., 1983, Simulation of solute transport in a mountain pool-and-riffle stream: A transient storage model: Water Resources Research, v. 19, p. 718-724.

Bernhardt, E.S., Palmer, M.A., Allan, J.D., Alexander, G., Barnas, K., Brooks, S., Carr, J., Clayton, S., Dahm, C., Follstad-Shah, J., Galat, D., Gloss, S., Goodwin, P., Hart, D., Hassett, B., Jenkinson, R., Katz, S., Kondolf, G.M., Lake, P.S., Lave, R., Meyer, J.L., O'Donnell, T.K., Pagano, L., Powell, B., and Sudduth, E., 2005, Ecology - Synthesizing US river restoration efforts: Science, v. 308, p. 636-637.

Boulton, A.J., Datry, T., Kasahara, T., Mutz, M., and Stanford, J.A., 2010, Ecology and management of the hyporheic zone: stream-groundwater interactions of running waters and their floodplains: Journal of the North American Benthological Society, v. 29, p. 26-40.

BOR (Bureau of Reclamation). 1988. Umatilla Basin Project, Oregon. Planning report, final environmental impact statement. Boise, Idaho.

Boyce, R. R. 1986. *A comprehensive plan for rehabilitation of anadromous fish stocks in the Umatilla river basin*. Final report of the Oregon Department of Fish and Wildlife to Bonneville Power Administration, Portland, Oregon. Publication DOE/BP-18008-1.

Brown, A. G. 1997. Biogeomorphology and diversity in multiple-channel river systems. Global Ecology and Biogeography Letters 6:179-185.

Buchanan, D.V. and S.V. Gregory 1997. *Development of water temperature standards to protect and restore habitat for bull trout and other cold water species in Oregon*. *Proceedings of the Friends of the Bull Trout Conference*. Calgary, Alberta.

Buffington, J.M., and Tonina, D., 2009. Hyporheic exchange in mountain rivers II: Effects of channel morphology on mechanics, scales and rates of exchange: Geography Compass, 3(3): 1038–1062.

Burkholder, B. K., Grant, G. E., Haggerty, R., Khangaonkar, T., and Wampler, P. J., 2008. Influence of hyporheic flow and geomorphology on temperature of a large, gravel-bed river, Clackamas River, Oregon, USA: Hydrological Processes 22: 941-953.

CHaMP (Columbia Habitat Monitoring Program). 2011. CHaMP 2011 training version 1.1.

CHaMP (Columbia Habitat Monitoring Program). 2012. Scientific protocol for salmonid habitat surveys within the Columbia Habitat Monitoring Program. Prepared by the Integrated Status and Effectiveness Monitoring Program and published by Terraqua, Inc., Wacounda, WA.

Contor, C. R. Editor. 2012. *Umatilla Basin Natural Production Monitoring and Evaluation, 2011 Annual Progress Report*. Confederated Tribes of the Umatilla Indian Reservation, 46411 Ti'Mine Way, Pendleton, OR. Report submitted to Bonneville Power Administration, Project No. 1990-005-01

Contor, C. R. Editor. 2016. *Umatilla Basin Natural Production Monitoring and Evaluation, 2016 Annual Progress Report*. Confederated Tribes of the Umatilla Indian Reservation, 46411 Ti'Mine Way, Pendleton, OR. Report submitted to Bonneville Power Administration, Project No. 1990-005-01

Crispell, J.K., Endreny, T.A., 2009, Hyporheic exchange flow around constructed in-channel structures and implications for restoration design: Hydrologic Processes: 23(8), 1158–1168.

CTUIR 1994. *Umatilla Basin Natural Production Monitoring and Evaluation, Annual Progress Report 1992-1993*. Prepared by Confederated Tribes of the Umatilla Indian Reservation and submitted to Bonneville Power Administration, Project No. 90-005-01.

CTUIR 1995. *Umatilla Basin Natural Production Monitoring and Evaluation*, Annual Report, 1993-1994, Prepared by Confederated Tribes of the Umatilla Indian Reservation for U.S. Department of Energy, Bonneville Power Administration, Environment, Fish and Wildlife, Portland, OR, April 1995, Project No. 90-005-01.

CTUIR 2000. *Umatilla Basin Natural Production Monitoring and Evaluation Project, Annual Progress Report 1997-1998*. Confederated Tribes of the Umatilla Indian Reservation, BPA Project No. 1990-005-01.

CTUIR 2005. *Confederated Tribes of the Umatilla Indian Reservation Water Code.* Prepared by the Confederated Tribes of the Umatilla Indian Reservation, Department of Natural Resources, as amended through Resolution No. 05-027 (March 7, 2005).

CTUIR 2005. *Confederated Tribes of the Umatilla Indian Reservation Total Maximum Daily Load for temperature and turbidity.* Prepared by the Confederated Tribes of the Umatilla Indian Reservation, Department of Natural Resources, Issued by the US Environmental Protection Agency, Region 10, July 2005. Available online at URL: http://yosemite.epa.gov/R10/WATER.NSF/TMDLs/Approved+TMDLs.

CTUIR 2007. *Biological Assessment, Birch Creek Salmonid Passage Improvements, Umatilla River Basin*. Prepared by the Confederated Tribes of the Umatilla Indian Reservation. July 2007.

CTUIR 2008. *Umatilla River Basin Anadromous Fish Habitat Enhancement Project*, *Annual Report, February 1, 2007 – January 31, 2008, Fiscal Year 2007,* Document ID# P109208, Contract # 32047. Confederated Tribes of the Umatilla Indian Reservation. Submitted to Bonneville Power Administration, January 2008. Available online as accessed January 22, 2009 at URL: http://pisces.bpa.gov/release/documents/documentviewer.aspx?doc=P109208.

CTUIR 2012. *Meacham Creek Floodplain Restoration and In-stream Enhancement Project Completion Report*. Published by Tetra Tech, Inc., Bothell, Washington. December 2012.

CTUIR 2012. *Umatilla Basin Natural Production Monitoring and Evaluation, 2011 Annual Progress Report*. Confederated Tribes of the Umatilla Indian Reservation, 46411 Ti'Mine Way, Pendleton, OR. Report submitted to Bonneville Power Administration, Project No. 1990-005-01

CTUIR 2016. *Birch Creek Watershed Action Plan*. Mission, Oregon. 115 pp.

CTUIR, ODEQ and UBWC. 2000. Umatilla River Basin Water Quality Analysis in Preparation for the Total Maximum Daily Load (TMDL). Umatilla Stakeholders and Technical Committee.

CTUIR, ODEQ and UBWC. 2000b. Public Comment Draft of the Umatilla River Basin Total Maximum Daily Load (TMDL) and Water Quality Management Plan (WQMP).

CTUIR and ODFW 2006. *Five-Year Action Plan for the Development and Maintenance of Habitat Improvement Projects in the Umatilla Subbasin: 2006-2010,* Prepared for/Funded by: U.S. Department of Energy, Bonneville Power Administration, and Division of Fish and Wildlife, March 2006.

Downes, B.J., L.A. Barmuta, P.G. Fairweather, D.P. Faith, M.J. Keough, P.S. Lake, B.C. Mapstone, G.P. Quinn. 2002. Monitoring Ecological Impacts: Concepts and Practices in Flowing Waters. Cambridge University Press, Cambridge, UK.

Ebersole, J. L., Liss, W. J., and Frissell, C. A., 2001, Relationship between stream temperature, thermal refugia, and rainbow trout Oncorhynchus mykiss abundance in arid-land streams in the northwestern United States: Ecology of Freshwater Fishes 10:1-10.

Environmental Protection Agency (1986). Quality Criteria for Water. http://water.epa.gov/scitech/swguidance/standards/criteria/aqlife/upload/2009_01_13_criteria_goldbook.pdf

Evans, E. C., and Petts, G. E., 1997, Hyporheic temperature patterns within riffles: Hydrological Sciences Journal 42:199-213.

Fernald, A. G., Landers, D. H., and Wigington, P. J., 2006, Water quality changes in hyporheic flow paths between a large gravel bed river and off-channel alcoves in Oregon, USA: River Research and Applications 22:1111-1124.

Fetter, C. W., Applied Hydrogeology, 3rd ed., 691 pp., Prentice-Hall, Englewood Cliffs, N. J., 1994. Geist, D. R. 2000. Hyporheic discharge of river water into fall Chinook salmon (Oncorhynchus tshawytscha) spawning areas in the Hanford Reach, Columbia River. Canadian Journal of Fisheries and Aquatic Sciences 57:1647-1656.

Freeze, A. R., and Cherry, J. A. (1979). *Groundwater*. Prentice Hall.

Geist, D. R., Hanrahna, T. P., Arntzen, E. V., McMichael, G. A., Murray, C. J., and Chien, Y., 2002, Physiochemical characteristics of the hyporheic zone affect redd site selection by chum salmon and fall Chinook salmon in the Columbia River: North American Journal of Fisheries Management, 22: 1107-1085.

Gooseff, M.N., Anderson, J.K., Wondzell, S., LaNier, J., and Haggerty, R., 2006, A modeling study of hyporheic exchange pattern and the sequence, size, and spacing of stream bedforms in mountain stream networks, Oregon, USA (Retraction of vol 19, pg 2915, 2005): Hydrological Processes, v. 20, p. 2441-+.

Haggerty, R., Wondzell, S.M., and Johnson, M.A., 2002, Power-law residence time distribution in the hyporheic zone of a 2nd-order mountain stream: Geophysical Research Letters, v. 29. Hanrahan, T. P., 2008, Effects of river discharge on hyporheic exchange flows in salmon spawning areas of a large gravel-bed river: Hydrological Processes 22:127-141.

Harbaugh, A.W., 2005, MODFLOW-2005, The U.S. Geological Survey modular ground-water model—the Ground-Water Flow Process: U.S. Geological Survey Techniques and Methods 6- A16

Harman, W., R. Starr, M. Carter, K. Tweedy, M. Clemmons, K. Suggs, C. Miller. 2012. A Function-Based Framework for Stream Assessment and Restoration Projects. US Environmental Protection Agency, Office of Wetlands, Oceans, and Watersheds, Washington, DC EPA 843-K-12-006.

Hester, E.T., and Gooseff, M.N., 2010, Moving Beyond the Banks: Hyporheic restoration is fundamental to restoring ecological services and functions of streams: Environmental Science and Technology: 44, 1521–1525.

Hester, E. T., Doyle, M. W., and Poole, G. C., 2009, The influence of in-stream structures on summer water temperature via induced hyporheic exchange: Limnology and Oceanography 51:355-367.

Hillman, T. W. 2003. Monitoring Strategy for the Upper Columbia Basin. BioAnalysts, Inc., Eagle, Idaho.

Hoehn, E., and Cirpka, O.A., 2006, Assessing residence times of hyporheic ground water in two alluvial flood plains of the Southern Alps using water temperature and tracers: Hydrology and Earth System Sciences, v. 10, p. 553-563.

Hoverson, Eric D. and Webster, James G. 2009. *CTUIR Umatilla Anadromous Fisheries Habitat Project Annual Report, Fiscal Year 2008*. Confederated Tribes of the Umatilla Indian Reservation, report submitted to Bonneville Power Administration, Project No. 1987-100-01.

Hubler, S. 2008. PREDATOR: Development and use of RIVPACS-type macroinvertebrate models to assess the biotic condition of wadeable Oregon streams. DEQ08-LAB-0048-TR.

Huff D.D., S.L. Hubler, Y. Pan, and D.L. Drake. 2006. Detecting Shifts in Macroinvertebrate Community Requirements: Implicating Causes of Impairment in Streams. Oregon Department of Environmental Quality. DEQ06-LAB-0068-TR.

Jones, K. L., G. C. Poole, E. J. Quaempts, S. O'Daniel, T. Beechie, 2008. *Umatilla River Vision.* Prepared for the Confederated Tribes of the Umatilla Indian Reservation, 31 pp.

Karr, J.R. and E.W. Chu. 1999. Restoring Life in Running Waters: Better Biological Monitoring. Island Press, Covelo, California.

Kasahara, T., Hill, A.R., 2006, Hyporheic exchange flows induced by constructed riffles and steps in lowland streams in southern Ontario, Canada: Hydrologic Processes: 20 (20), 4287–4305.

Kondolf, G.M., D.R. Montgomery, H. Piegay, and L. Schmitt. 2003. Geomorphic classification of rivers and streams, in Tools in Fluvial Geomorphology, edited by G.M. Kondolf and H. Piegay, pp. 171-204, John Wiley, Hoboken, NJ.

Lambert, Michael B. and Keith Karoglanian. 2012. The Umatilla Anadromous Fish Habitat Project: 2011 Annual Progress Report. Confederated Tribes of the Umatilla Indian Reservation, report submitted to Bonneville Power Administration, Project No. 1987-100-01.

Lambert, Michael B., James G. Webster, and Eric D. Hoverson. 2011. The Umatilla Anadromous Fish Habitat Project: 2009-2010 Annual Report. Confederated Tribes of the Umatilla Indian Reservation, report submitted to Bonneville Power Administration, Project No. 1987-100-01.

Lamontagne, S., and Cook, P.G., 2007, Estimation of hyporheic water residence time in situ using Rn-222 disequilibrium: Limnology and Oceanography-Methods, v. 5, p. 407-416.

Lucier, A., M. Palmer, H. Mooney, K. Nadelhoffer, D. Ojima, and F. Chavez. 2006. Ecosystems and Climate Change Research Priorities for the U.S. Climate Change Science Program, Special Series No. SS-92-06 of the University of Maryland Center for Environmental Science, Chesapeake Biological Laboratory, Ref. No. [UMCES] CBL 06-038. 50 pp.

Malcolm, I. A., Soulsby, C., Youngson, A. F., and Petry, J., 2003, Heterogeneity in ground water-surface water interactions in the hyporheic zone of a salmonid spawning stream: Hydrological Processes 17:601-617.

Merritt, R.W., K.W. Cummins, and M.B. Berg (eds.) 2008. An Introduction to the Aquatic Insects of North America, 4th edition. Kendall/Hunt Publishing Company, Dubuque, IA.

Miller, S.W., P. Budy, and J.C. Schmidt. 2010. Quantifying macroinvertebrate responses to in-stream habitat restoration: applications of meta-analysis to river restoration. Restoration Ecology 18: 8-19.

Montgomery, D.R., and J.M. Buffington, 1997. Channel-reach morphology in mountain drainage basins. Geological Society of America Bulletin 109(5):596-611.

Montgomery, David R. 2003. *King of Fish: The Thousand Year Run of Salmon*. Westview Press, Perseus Books Group, Boulder, Colorado.

Moore, Kelley M.S., Jones, Kim, K. Dambacher, Jeffrey M. 2002. *Methods for stream habitat surveys version 12.1: Oregon Department of Fish and Wildlife, Aquatic Inventory Project*. Corvallis, OR 97730.

Morrill JC, Bales RC, Conklin MH (2005) Estimating stream temperature from air temperature: implications for future water quality. J Environ Eng 131:139–145

Nagle, G. 1998. *Report on research project on environmental history of riparian areas in the Umatilla basin*. U.S. Forest Service, Pacific Northwest Research Station, Corvallis, Oregon.

NMFS 1996. *Making Endangered Species Act determinations of effect for individual or grouped actions at the watershed scale*. NMFS Environmental and Technical Services Division, Habitat Conservation Branch.

NMFS 2008. National Marine Fisheries Service Northwest Region. *Endangered Species Act – Section 7 Programmatic Consultation Biological Opinion and Magnuson-Stevens Fishery Conservation and Management Act Essential Fish Habitat Consultation.* Habitat Improvement Program, Oregon, Washington, and Idaho, CY2007-CY2012 (HIP II).

NMFS (National Marine Fisheries Service) Northwest Region. 2009. Middle Columbia Steelhead distinct Population Segment ESA Recovery Plan. Final Listing November 30, 2009. Available on the internet: http://www.nwr.noaa.gov/Salmon-Recovery-Planning/Recovery-Domains/Interior-Columbia/Mid-Columbia/upload/Mid-C-Plan.pdf

NPCC 1990. Northwest Power Planning Council. *Umatilla River Subbasin Salmon and Steelhead Production Plan*. Northwest Power Planning Council and the Agencies of the Indian Tribes of the Columbia Basin Fish and Wildlife Authority.

NPCC (Northwest Power Conservation Council). 2004. *Draft Willow/Umatilla Subbasin Plan*, Prepared by the Umatilla/Willow Subbasin Planning Team. Prepared for the Northwest Power and Conservation Council, May 28, 2004. Available online from the following URL as accessed November 19, 2008: http://www.nwcouncil.org/fw/subbasinplanning/umatilla/plan/.

NPCC (Northwest Power Conservation Council). 2005. *Final Umatilla Willow Subbasin Plan*. Prepared by the Umatilla/Willow Subbasin Planning Team, for the Northwest Power and Conservation Council, May, 2005.

NRC 1996. *Upstream. Salmon and society in the Pacific Northwest*. National Research Council, Washington D.C.

O'Daniel, S., J. 2005. Interactions between Regional-Scale Variation in Geomorphology and Potential for Hyporheic Exchange along the Umatilla River, Oregon. Geography. Santa Barbara, University of California.

O'Daniel, S.J., G.C. Poole and L.A.K. Mertes. 2003. Habitat diversity in alluvial rivers, Report to Bonneville Power Administration, #200100252, 39 pp.

ODEQ (Oregon Department of Environmental Quality) and Confederated Tribes of the Umatilla Indian Reservation. 2001. Umatilla River Basin Total Maximum Daily Load and Water Quality Management Plan. http://www.deq.state.or.us/wq/tmdls/docs/umatillabasin/umatilla/tmdl.pdf

ODFW/ODF (Oregon Department of Fish and Wildlife/Oregon Department of Forestry). 1995. A Guide to Placing Large Wood in Streams.

ODFW/ODF (Oregon Department of Fish and Wildlife/Oregon Department of Forestry). 1999. Oregon Aquatic Habitat Restoration and Enhancement Guide.

OWRD (Oregon Water Resource Department). 2006. Estimation of Peak Discharges for Rural, Unregulated Streams in Eastern Oregon. Salem, OR.

Peck, D.V., A.T. Herlihy, B.H. Hill, R.M. Hughes, P.R. Kaufmann, D.J. Klemm, J.M. Lazorchak, F.H. McCormick, S.A. Peterson, P.L. Ringold, T. Magee, and M.R. Cappaert. 2006. Environmental Monitoring and Assessment Program – Surface Waters; Western Pilot Study: Field Operations Manual for Wadeable Streams. U.S. Environmental Protection Agency 620/R-06/003. Office of Research and Development, U.S. Environmental Protection Agency, Washington D.C.

Phinney, W. 2017. *Tribes play big role in Dillon Dam removal*. Confederated Umatilla Journal. August 2017: 5A. Print.

Plaven, G. 2017 *Dam near gone*. East Oregonian. 22 July 2017: A1. Print

Pollock, D.W. 2008. User's guide for MODPATH/MODPATH-PLOT, version 3: a particle tracking post-processing package for MODFLOW, the U.S. Geological Survey finite-difference ground-water flow model. USGS Open-File Report 94-464.

Poole, G.C., O'Daniel, S.J., Jones, K.L., Woessner, W.W., Bernhardt, E.S., Helton, A.M., Stanford, J.A., Boer, B.R., and Beechie, T.J. 2008. Hydrologic spiraling: The role of multiple interactive flow paths in stream ecosystems: River Research and Applications, v. 24, p. 1018-1031.

Purser, Michael D. 1994. Non-point Sources of Water Pollution Assessment and Management Plan. Submitted by the Confederated Tribes of the Umatilla Indian Reservation to the U.S. Environmental Protection Agency.

Quaempts, E. J., K. L. Jones, S. J. O'Daniel, T. J. Beechie, and G. C. Poole. 2018. *Aligning environmental management with ecosystem resilience: a First Foods example from the Confederated Tribes of the Umatilla Indian Reservation, Oregon, USA.* Ecology and Society 23(2):29.

Rollins, P.A., Editor. 1935. *The Discovery of the Oregon Trail. Robert Stuart's Narratives of His Overland Trip Eastwards from Astoria in 1812-13*. University of Nebraska Press, Lincoln, Nebraska.

Roni, Phil, Beechie T. J., Bilby R. E., Leonetti F. E., Pollock M. M., and Pess G. R. 2002. "A review of stream restoration techniques and a hierarchical strategy for prioritizing restoration in Pacific Northwest watersheds." North American Journal of Fisheries Management.

Roni, Phil, Hanson K., and Beechie T. 2008. *Global review of the physical and biological effectiveness of stream habitat restoration rehabilitation techniques.* North American Journal of Fisheries Management.

Rosgen, D.L., 1994, A classification of natural rivers: Catena, v. 22, p. 169-199. Stanford, J. A., Ward, J. V., Liss, W. J., Frissell, C. A., Williams, R. N., Lichatowich, J. A., and Coutant, C. C., 1996, A general protocol for restoration of regulated rivers. Regulated Rivers: Research and Management 12:391-413.

Rosgen, D.L. (1996) *Applied River Morphology*. Wildland Hydrology, Pagosa Springs, CO.

Smith, E.P. 2002. BACI Design. pp. 141-148. In: A.H.E.-S.a.W.W. Piegorsc (ed.) *Encyclopedia of Environmetrics*, John Wiley & Sons, Ltd, Chichester, 2002.

Stanford, J. A., and Ward, J. V., 1993, An ecosystem perspective of alluvial rivers: connectivity and the hyporheic corridor: Journal of the North American Benthological Society 12:48-60.

Stonestrom, D. A. and Constantz, J. 2003. Heat as a tool for studying the movement of ground water near streams. U.S. Geological Survey Circular 1260, 96 p

Stillwater Sciences. 2011. Biological effectiveness monitoring and evaluation plan for fisheries habitat enhancement in CTUIR subbasins. Draft Report. Prepared by Stillwater Sciences, Portland, Oregon for Confederated Tribes of the Umatilla Indian Reservation, Pendleton, Oregon.

Taylor, George H. 1993. *Normal Annual Precipitation, State of Oregon, Period 1961-1990, Map.* Oregon Climate Service, 326 Strand Ag. Hall, Oregon State University, Corvallis, Oregon 97331-2209.

Tetra Tech 2010. *Final Biological Assessment Meacham Creek Floodplain Restoration and In-stream Enhancement Project River Mile 6 to 7*. Prepared for the Confederated Tribes of the Umatilla Indian Reservation, Pendleton, OR.

Tetra Tech 2012. *Meacham Creek Vegetation Monitoring Strategy and Survey Protocol*. Prepared for the Confederated Tribes of the Umatilla Indian Reservation, Pendleton, OR.

Tetra Tech 2013. Meacham Creek Floodplain Restoration and In-Stream Enhancement Design (Phase II) Implementation Plan (100 percent) Revision 1 Package.

Tetra Tech. 2013a. Meacham Creek Columbia Habitat Monitoring Program (CHaMP) Monitoring 2012 Baseline Report. Prepared for the Confederated Tribes of the Umatilla Indian Reservation. January 2013.

Tetra Tech. 2013b. Meacham Creek Floodplain Restoration and In-Stream Enhancement 2012 Monitoring Data. Prepared for the Confederated Tribes of the Umatilla Indian Reservation. January 2013.

Thorp, J.H. and Covich, A.P. (eds.) 2010. Ecology and Classification of North American Freshwater Invertebrates, 3rd edition. Academic Press, Inc., San Diego, CA.

Three Treaty Tribes & FCRPS Action Agencies. 2008. *Columbia Basin Fish Accords, Memorandum of Agreement Among the Umatilla, Warm Springs and Yakama Tribes, Bonneville Power Adminstration, U.S. Army Corps of Engineers, and U.S. Bureau of Reclamation*. Prepared collectively "the Parties", May, 2008. Available online from the following URL as accessed January 28, 2013: www.salmonrecovery.gov/Files/BiologicalOpinions/MOA_ROD.pdf

Tonina, D., and Buffington, J.M., 2007, Hyporheic exchange in gravel bed rivers with pool-riffle morphology: Laboratory experiments and three-dimensional modeling: Water Resources Research, v. 43.

Tonina, D., and Buffington, J.M., 2009, Hyporheic exchange in mountain rivers I: mechanics and environmental effects: Geography Compass 3(3): 1063–1086.

Torgersen, C. E., D. M. Price, H. W. Li, and B. A. McIntosh. 1999. Multiscale thermal refugia and stream habitat associations of Chinook Salmon in northeastern Oregon. Ecological Applications 9:301-319.

Toth, J., 1963, A theoretical analysis of groundwater flow in small drainage basins: Journal of Geophysical Research, v. 68, p. 4795-4812.

Treaty of 1855. *Treaty with the Wallawalla, Cayuse, etc., 1855*, June 9, 1855, 12 Stats., 945, Ratified Mar. 8, 1859.

Umatilla National Forest. 2001. Umatilla and Meacham Ecosystem Analysis. https://scholarsbank.uoregon.edu/xmlui/bitstream/handle/1794/6779/Umatilla_Meacham_Vegetation_Analysis.pdf?sequence=1

USFWS 2002. *Bull Trout* (*Salvelinus confluentus*) *Draft Recovery Plan*. U. S. Fish and Wildlife Service, Portland, Oregon. Paged by section. Available online from URL: http://ecos.fws.gov/docs/recovery_plans/2002/021129.pdf.

USFWS 2007. *Biological Opinion and Letter of Concurrence, USDA Forest Service, USDI Bureau of Land Management and the Coquille Indian Tribe for Programmatic Aquatic Habitat Restoration Activities in Oregon and Washington that Affect ESA-listed Fish, Wildlife, and Plant Species and their Critical Habitats.* US Fish and Wildlife Service, Lead Office: Oregon Fish and Wildlife Office, Portland, Oregon.

USFWS 2015. *Recovery plan for the coterminous United States population of bull trout (*Salvelinus confluentus*)*. U.S. Fish and Wildlife Service, Portland, Oregon. Avaialable online from: https://www.fws.gov/pacific/bulltrout/pdf/Final_Bull_Trout_Recovery_Plan_092915.pdf

USGS (U.S. Geological Survey). 2006. User's Manual for Program PeakFQ, Annual Flood-Frequency Analysis Using Bulletin 17B Guidelines.

USGS 2008. United States Geological Survey. “Columbia Plateau, Columbia River Basalt”, as accessed November 19, 2008 from URL: http://vulcan.wr.usgs.gov/Volcanoes/ColumbiaPlateau/description_columbia_plateau.html.

Walker, George W. and Norman S. MacLeod. 1991. *Geologic Map of Oregon*, U.S. Geological Survey, U.S. Department of the Interior, U.S. Geological Survey Map Distribution, Box 25286, Federal Center, Denver, CO 80225.

Ward, J. V., 1989, The four-dimensional nature of lotic ecosystems: Journal of the North American Benthological Society 8:2-8.

White, D. S., Elzinga, C. H., and Hendricks, S. P., 1987, Temperature patterns within the hyporheic zone of a northern Michigan river: Journal of the North American Benthological Society 6:85-91.

White, T., Jewett, S., Hanson, J., Carmichael, R., 1989, Evaluation of juvenile salmonid outmigration and survival in the lower Umatilla River basin: Project No. 1989- 02401, 122 electronic pages, (BPA Report DOE/BP-00004340-3).

Whitney, L. 2007. Upper Grande Ronde Basin, Section 319, National Monitoring Program Project: Summary Report. Oregon Department of Environmental Quality Technical Report DEQ07-LAB-0058-TR. Oregon Department of Environmental Quality, Portland, Oregon.

Whittier, T.R. and J. Van Sickle. 2010. Macroinvertebrate tolerance values and an assemblage tolerance index (ATI) for western USA streams and rivers. Journal of the North American Benthhological Society 29: 852-866.

Wiggins, G.B. 2000. Larvae of the North American Caddisfly General (Trichoptera), 2nd edition. University of Toronto Press, Toronto.

Wilcock, Peter; John Pitlick; Yantao Cui. 2009. Sediment transport primer: estimating bed-material transport in gravel-bed rivers. Gen. Tech. Rep. RMRS-GTR-226. Fort Collins, CO: U.S. Department of Agriculture, Forest Service, Rocky Mountain Research Station. 78 p.

Wohl, E., Angermeier, P.L., Bledsoe, B., Kondolf, G.M., MacDonnell, L., Merritt, D.M., Palmer, M.A., Poff, N.L., and Tarboton, D., 2005, River restoration: Water Resources Research, v. 41.

Wondzell, S.M., and Swanson, F.J., 1996, Seasonal and storm dynamics of the hyporheic zone of a 4th-order mountain stream .2. Nitrogen cycling: Journal of the North American Benthological Society, v. 15, p. 20-34.

Wondzell, S.M., LaNier, J., and Haggerty, R. 2009. Evaluation of alternative groundwater flow models for simulating hyporheic exchange in a small mountain stream. Journal of Hydrology, v. 364, p. 142-151.

APPENDIX A: USE OF DATA AND PRODUCTS

Umatilla Projects Review

http://pisces.bpa.gov/release/documents/documentviewer.aspx?doc=P130848

APPENDIX B: LIST OF METRICS AND INDICATORS

Category	Subcategory	Subcategory Focus 1	Subcategory Focus 2	Specific Metric Title
Classification of Ecological or Geological Attribute	Form/Morphology	Habitat Type: Channels		Channel Complexity
Classification of Ecological or Geological Attribute	Form/Morphology	Habitat Type: Channels		Channel Score
Classification of Ecological or Geological Attribute	Form/Morphology	Habitat Type: Channels		Channel Unit Volume
Classification of Ecological or Geological Attribute	Form/Morphology	Habitat Type: Channels		Residual Pool Volume
Fish	Prey Availability for Fish Species			Growth Potential
Hydrology/Water Quantity	Flow			Discharge
Hydrology/Water Quantity	Flow			Velocity Heterogeneity
Landscape Form & Geomorphology	Composition/Structure of Habitat Types	Habitat Type: Channels		Channel Unit Complexity
Landscape Form & Geomorphology	Composition/Structure of Habitat Types	Habitat Type: Channels		Channel Unit Volumes
Landscape Form & Geomorphology	Composition/Structure of Habitat Types	Habitat Type: Channels		Channel Unit Complexity
Landscape Form & Geomorphology	Cover	Habitat Type: Channels		Percent fish cover
Landscape Form & Geomorphology	Cover	Habitat Type: Channels		Fish Cover
Landscape Form & Geomorphology	Density of Habitat Type	Habitat Type: Channels		Pool Frequency
Landscape Form & Geomorphology	Density of Instream Wood			Channel unit large wood volume
Landscape Form & Geomorphology	Density of Instream Wood			Channel unit large wood

				volume/count in log jams
Landscape Form & Geomorphology	Density of Instream Wood			Site large wood volume
Landscape Form & Geomorphology	Depth: Bathymetry			Thalweg Profile
Landscape Form & Geomorphology	Depth: Pool			Residual Pool Depth
Landscape Form & Geomorphology	Distribution of Habitat Type	Habitat Type: Channel: Pools		Percent Pools
Landscape Form & Geomorphology	Distribution of Habitat Type	Habitat Type: Channel: Pools		Pool Frequency
Landscape Form & Geomorphology	Distribution of Instream Wood			LWD Volume
Landscape Form & Geomorphology	Edge/Density/Sinuosity	Habitat Type: Channels		Sinuosity
Landscape Form & Geomorphology	Gradient			Gradient
Landscape Form & Geomorphology	Size: Wood Structure			Residual Pool Volume
Landscape Form & Geomorphology	Width to Depth Ratio			Bankfull width-to-depth ratio
Landscape Form & Geomorphology	Width to Depth Ratio			Wetted width-to-depth ratio
Landscape Form & Geomorphology	Width: Bankfull			Bankfull Width
Light	Light Concentration			Riparian cover
Light	Light Concentration			Solar Input
Macroinvertebrates	Drift Density	Habitat Type: Channels		Drift biomass
Macroinvertebrates	Drift Density	Habitat Type: Channels		Total Drift Biomass
Sediment/Substrate/Soils	Composition: Substrate/Soil-Dominant Size			Percentage substrate composition

Sediment/Substrate/Soils	Composition: Substrate/Soil-Dominant Size			Riffle Particle Size (D16, D50, D84)
Sediment/Substrate/Soils	Composition: Substrate/Soil-Dominant Type			Percent Fines
Sediment/Substrate/Soils	Depth-Fines			Subsurface Fines
Sediment/Substrate/Soils	Distribution of Sediment			Riffle Particle Size (D16, D50, D84)
Sediment/Substrate/Soils	Embeddedness			Percent cobble embedded
Sediment/Substrate/Soils	Embeddedness			Embeddedness of Fast water Cobble
Vegetation/Plants	Composition: Vegetative Species Assemblage			Riparian Structure
Vegetation/Plants	Density of Vegetation			Riparian Structure
Water Quality	Alkalinity	Habitat Type: Channels		Alkalinity
Water Quality	Alkalinity	Habitat Type: Channels		Average Alkalinity
Water Quality	Conductivity			Conductivity
Water Quality	Conductivity			Average Conductivity
Hydrology/Water Quantity	Flow			Radon 222 Geochemistry
Hydrology/Water Quantity	Ground Water Level Change			Groundwater Surface Elevation
Hydrology/Water Quantity	Hyporheic Flow			Groundwater Budget Model
Water Quality	Water Temperature			Groundwater Temperature
Water Quality	Water Temperature			Surface Water Temperature
